




Appendix G - Noise Monitoring Results

Location NC1 - True Light Middle School of Hong Kong							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
5-Aug-08	12:55	Cloudy	66.8	70.0	60.5	70.2	66.8, Measured ≤ Baseline
12-Aug-08	14:00	Cloudy	67.7	69.5	62.5		67.7, Measured ≤ Baseline
19-Aug-08	14:20	Cloudy	69.7	72.0	67.0		69.7, Measured ≤ Baseline
25-Aug-08	14:05	Cloudy	68.9	71.5	65.0		68.9, Measured ≤ Baseline

Location NC2 - The Legend							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
5-Aug-08	13:35	Cloudy	65.9	67.0	64.5	64.8	59.4
12-Aug-08	14:45	Cloudy	72.3	74.5	68.0		71.4
19-Aug-08	15:00	Cloudy	68.9	70.5	64.5		66.8
25-Aug-08	14:40	Cloudy	73.6	76.0	69.0		73.0

Location NC3 - Outside Aegean Terrace							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
5-Aug-08	14:45	Cloudy	57.3	58.5	51.5	57.7	57.3, Measured ≤ Baseline
12-Aug-08	16:25	Cloudy	57.8	58.5	53.5		41.4
19-Aug-08	16:30	Cloudy	58.8	60.0	52.5		52.3
25-Aug-08	16:45	Cloudy	58.2	59.5	56.5		48.6

Noise Levels

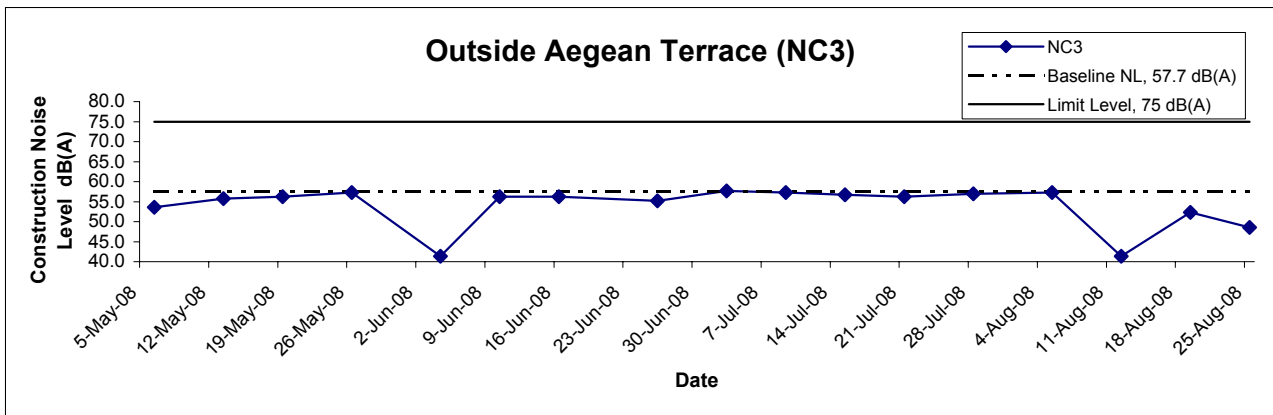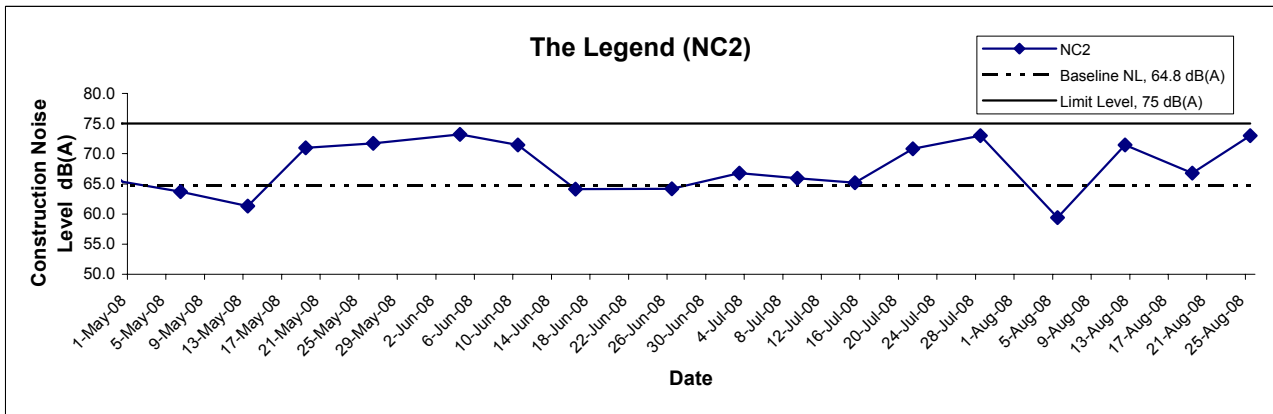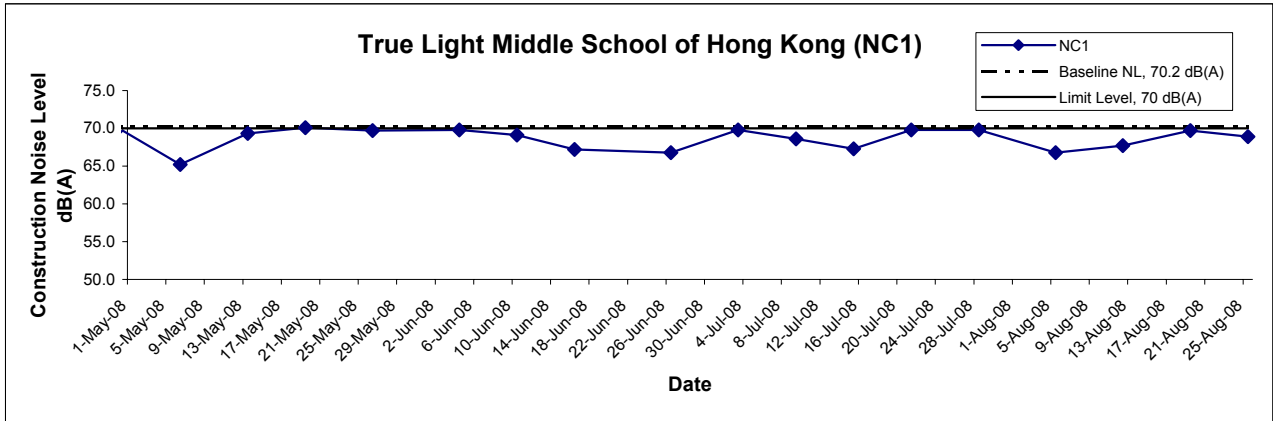

Title Contract No. DC/2007/10 Design and Construction of Hong Kong West Drainage Tunnel Graphical Presentation of Construction Noise Monitoring Results	Scale	Project	
	N.T.S	No. MA8001	
	Date	Appendix	
	Aug 08	G	
