




Appendix G - Noise Monitoring Results

Location NC1 - True Light Middle School of Hong Kong							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
3-Jul-08	15:40	Sunny	69.8	72.5	66.5	70.2	69.8, Measured ≤ Baseline
9-Jul-08	15:30	Cloudy	68.6	70.5	66.0		68.6, Measured ≤ Baseline
15-Jul-08	11:35	Sunny	67.3	69.5	64.5		67.3, Measured ≤ Baseline
21-Jul-08	10:45	Sunny	69.8	71.5	65.5		69.8, Measured ≤ Baseline
28-Jul-08	13:30	Sunny	73.0	76.0	67.5		69.8

Location NC2 - The Legend							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
3-Jul-08	15:00	Sunny	68.9	72.0	66.5	64.8	66.8
9-Jul-08	16:10	Cloudy	68.4	71.5	66.0		65.9
15-Jul-08	10:50	Sunny	68.0	68.5	67.0		65.2
21-Jul-08	11:35	Sunny	71.8	74.0	66.5		70.8
28-Jul-08	14:35	Sunny	73.6	76.5	68.5		73.0

Location NC3 - Outside Aegean Terrace							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
3-Jul-08	13:35	Sunny	57.7	59.0	50.5	57.7	57.7, Measured ≤ Baseline
9-Jul-08	13:20	Cloudy	57.3	59.0	51.5		57.3, Measured ≤ Baseline
15-Jul-08	13:00	Sunny	56.7	57.5	51.0		56.7, Measured ≤ Baseline
21-Jul-08	13:00	Sunny	56.2	57.5	50.5		56.2, Measured ≤ Baseline
28-Jul-08	16:00	Sunny	57.0	58.5	55.0		57.0, Measured ≤ Baseline

Noise Levels

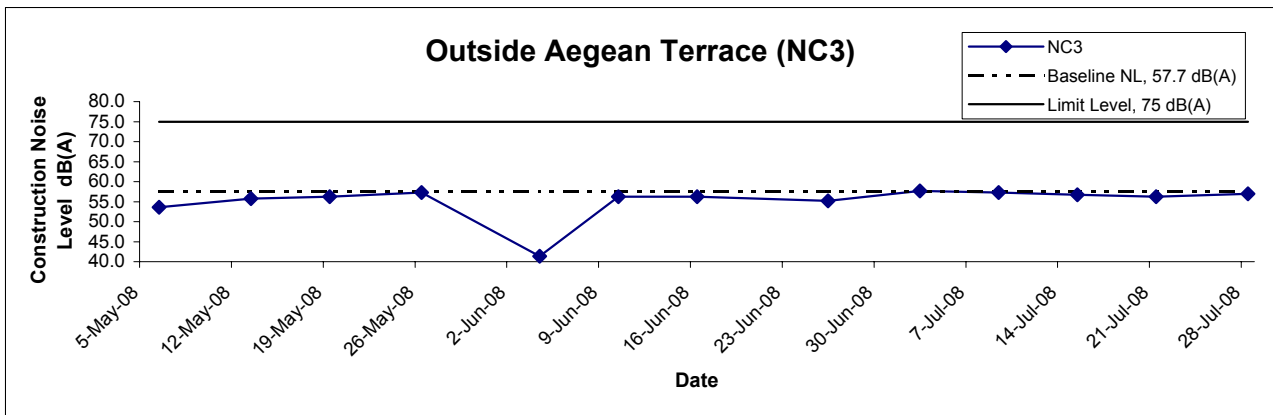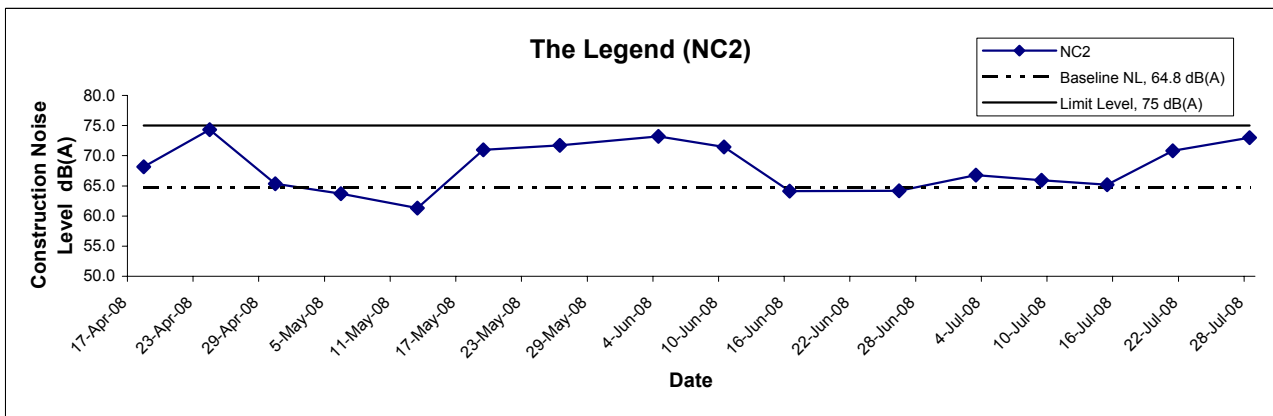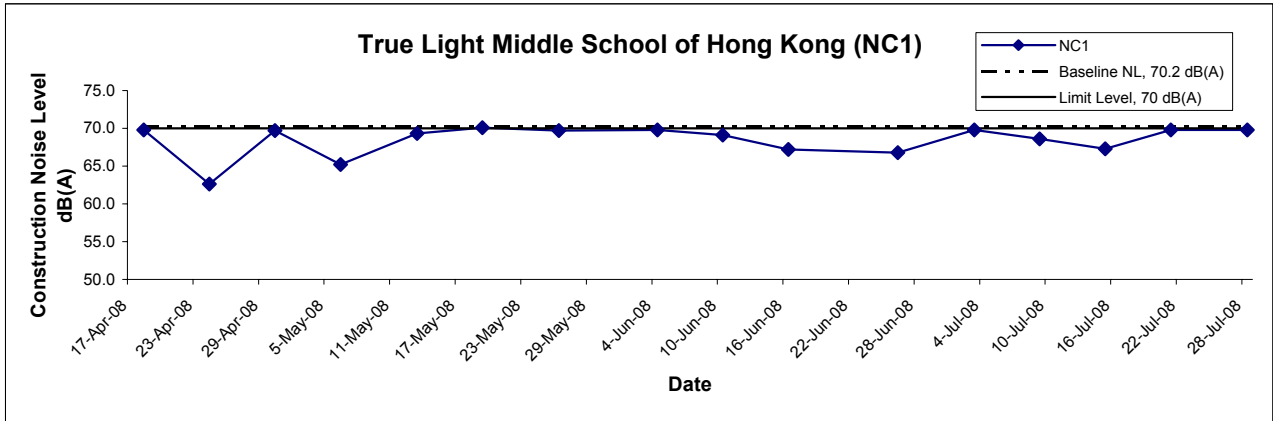

Title	Contract No. DC/2007/10	Scale	Project	CINOTECH
	Design and Construction of Hong Kong West Drainage Tunnel	N.T.S	No. MA8001	
Graphical Presentation of Construction Noise Monitoring Results		Date	Appendix	
		Jul 08	G	
