


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel


Air Quality Impact Monitoring Results (1-Hour TSP)

| Location | Monitoring Date | Weather Conditions | Wind Speed with Direction (m/s) | Temp (°C) | Timer-I (m) | Timer-F (m) | Time (mins) | Flow-I (CFM) | Flow-F (CFM) | Flow-I (m³/min) | Flow-F (m³/min) | Flow-avg (m³/min) | Volume (m³) | Weight-I (g) | Weight-F (g) | Weight-diff. (g) | 1-hr TSP (µg/m³) | Average 1-Hr TSP (µg/m³) | Action/Limit Levels (µg/m³) | Observation / Site Condition | Remark | |
|--|---|--------------------|---------------------------------|-----------|-------------|-------------|-------------|--------------|--------------|-----------------|-----------------|-------------------|-------------|--------------|--------------|------------------|------------------|--------------------------|-----------------------------|---|-----------------------|---------|
| Sik Sik Yuen Ho Fung College - Intake (ASR1) | 3-Jan-09 | Fine | 0.8NE | 17 | 567139 | 567239 | 60.0 | 40 | 40 | 1.36 | 1.36 | 1.36 | 81.54 | 2.8501 | 2.8549 | 0.0048 | 58.9 | 72.4 | 306.6/500 | Piling | Traffic | |
| | | Fine | 0.6NE | 17 | 567239 | 567339 | 60.0 | 40 | 40 | 1.36 | 1.36 | 1.36 | 81.54 | 2.8264 | 2.8331 | 0.0067 | 82.2 | | | | | |
| | | Fine | 0.6NE | 17 | 567339 | 567439 | 60.0 | 40 | 40 | 1.36 | 1.36 | 1.36 | 81.54 | 2.8391 | 2.8453 | 0.0062 | 76.0 | | | | | |
| | 9-Jan-09 | Sunny | 0.7E | 12 | 567439 | 567539 | 60.0 | 40 | 40 | 1.36 | 1.36 | 1.36 | 81.54 | 2.8813 | 2.8931 | 0.0118 | 144.7 | 124.7 | 306.6/500 | Nil | Traffic | |
| | | Sunny | 0.7E | 12 | 567539 | 567639 | 60.0 | 40 | 40 | 1.36 | 1.36 | 1.36 | 81.54 | 2.8544 | 2.8613 | 0.0069 | 84.6 | | | | | |
| | | Sunny | 0.7E | 12 | 567639 | 567739 | 60.0 | 40 | 40 | 1.36 | 1.36 | 1.36 | 81.54 | 2.8573 | 2.8671 | 0.0118 | 144.7 | | | | | |
| | 15-Jan-09 | Sunny | 0.6NE | 14 | 567739 | 567839 | 60.0 | 40 | 40 | 1.36 | 1.36 | 1.36 | 81.54 | 2.8243 | 2.8344 | 0.0101 | 123.9 | 99.3 | 306.6/500 | Nil | Traffic | |
| | | Sunny | 0.6NE | 14 | 567839 | 567939 | 60.0 | 40 | 40 | 1.36 | 1.36 | 1.36 | 81.54 | 2.8118 | 2.8187 | 0.0069 | 84.6 | | | | | |
| | | Sunny | 0.6NE | 14 | 567939 | 568039 | 60.0 | 40 | 40 | 1.36 | 1.36 | 1.36 | 81.54 | 2.8415 | 2.8488 | 0.0073 | 89.5 | | | | | |
| | 21-Jan-09 | Sunny | 0.7NE | 23 | 568039 | 568139 | 60.0 | 40 | 40 | 1.36 | 1.36 | 1.36 | 81.54 | 2.8707 | 2.8764 | 0.0057 | 69.9 | 92.0 | 306.6/500 | Nil | Traffic | |
| | | Sunny | 0.7NE | 23 | 568139 | 568239 | 60.0 | 40 | 40 | 1.36 | 1.36 | 1.36 | 81.54 | 2.8470 | 2.8569 | 0.0099 | 121.4 | | | | | |
| | | Sunny | 0.7NE | 23 | 568239 | 568339 | 60.0 | 40 | 40 | 1.36 | 1.36 | 1.36 | 81.54 | 2.8737 | 2.8866 | 0.0069 | 84.6 | | | | | |
| | 24-Jan-09 | Cloudy | 0.6NE | 16 | 568339 | 568439 | 60.0 | 40 | 40 | 1.36 | 1.36 | 1.36 | 81.54 | 2.8478 | 2.8523 | 0.0045 | 55.2 | 67.4 | 306.6/500 | Nil | Traffic | |
| | | Cloudy | 0.6NE | 16 | 568439 | 568539 | 60.0 | 40 | 40 | 1.36 | 1.36 | 1.36 | 81.54 | 2.8893 | 2.8950 | 0.0057 | 69.9 | | | | | |
| | | Cloudy | 0.6NE | 16 | 568539 | 568639 | 60.0 | 40 | 40 | 1.36 | 1.36 | 1.36 | 81.54 | 2.8806 | 2.8869 | 0.0063 | 77.3 | | | | | |
| | 29-Jan-09 | Cloudy | 0.5NE | 16 | 568639 | 568739 | 60.0 | 40 | 40 | 1.36 | 1.36 | 1.36 | 81.54 | 2.7261 | 2.7321 | 0.0060 | 73.6 | 105.5 | 306.6/500 | Nil | Nil | |
| | | Cloudy | 0.5NE | 16 | 568739 | 568839 | 60.0 | 40 | 40 | 1.36 | 1.36 | 1.36 | 81.54 | 2.7271 | 2.7354 | 0.0083 | 101.8 | | | | | |
| | | Cloudy | 0.5NE | 16 | 568839 | 568939 | 60.0 | 40 | 40 | 1.36 | 1.36 | 1.36 | 81.54 | 2.7485 | 2.7600 | 0.0115 | 141.0 | | | | | |
| | Hong Hoi Chee Hong Temple - Intake (ASR3) | 3-Jan-09 | Cloudy | 0.5N | 15 | 535589 | 535689 | 60.0 | 40 | 40 | 1.39 | 1.39 | 1.39 | 83.68 | 2.7481 | 2.7532 | 0.0051 | 63.9 | 69.7 | 327.4/500 | Set up piling | Nil |
| | | | Cloudy | 0.5N | 15 | 535689 | 535789 | 60.0 | 40 | 40 | 1.39 | 1.39 | 1.39 | 83.68 | 2.8578 | 2.8649 | 0.0071 | 84.8 | | | | |
| | | | Cloudy | 0.5N | 15 | 535789 | 535889 | 60.0 | 40 | 40 | 1.39 | 1.39 | 1.39 | 83.68 | 2.8479 | 2.8532 | 0.0053 | 63.3 | | | | |
| | | 9-Jan-09 | Sunny | 0.6N | 12 | 535889 | 535990 | 60.6 | 40 | 40 | 1.39 | 1.39 | 1.39 | 84.52 | 2.8643 | 2.8704 | 0.0061 | 72.2 | 120.9 | 327.4/500 | Piling | Nil |
| | | | Sunny | 0.6N | 12 | 535990 | 536095 | 57.0 | 40 | 40 | 1.39 | 1.39 | 1.39 | 79.50 | 2.8732 | 2.8866 | 0.0134 | 168.6 | | | | |
| | | | Sunny | 0.6N | 12 | 536095 | 536186 | 60.6 | 40 | 40 | 1.39 | 1.39 | 1.39 | 84.52 | 2.8531 | 2.8634 | 0.0103 | 121.9 | | | | |
| 15-Jan-09 | | Sunny | 0.7N | 14 | 536186 | 536295 | 60.0 | 40 | 40 | 1.39 | 1.39 | 1.39 | 83.68 | 2.8918 | 2.8972 | 0.0054 | 64.5 | 75.7 | 327.4/500 | Piling | Nil | |
| | | Sunny | 0.7N | 14 | 536295 | 536389 | 60.0 | 40 | 40 | 1.39 | 1.39 | 1.39 | 83.68 | 2.8856 | 2.8721 | 0.0065 | 77.7 | | | | | |
| | | Sunny | 0.7N | 14 | 536389 | 536489 | 60.0 | 40 | 40 | 1.39 | 1.39 | 1.39 | 83.68 | 2.8336 | 2.8407 | 0.0071 | 84.8 | | | | | |
| 21-Jan-09 | | Sunny | 0.4NE | 17 | 536489 | 536589 | 60.0 | 40 | 40 | 1.39 | 1.39 | 1.39 | 83.68 | 2.8650 | 2.8715 | 0.0065 | 77.7 | 66.1 | 327.4/500 | Piling , breaking by backhoe | Nil | |
| | | Sunny | 0.4NE | 17 | 536589 | 536689 | 60.0 | 40 | 40 | 1.39 | 1.39 | 1.39 | 83.68 | 2.8557 | 2.8405 | 0.0048 | 57.4 | | | | | |
| | | Sunny | 0.4NE | 17 | 536689 | 536789 | 60.0 | 40 | 40 | 1.39 | 1.39 | 1.39 | 83.68 | 2.9074 | 2.9127 | 0.0053 | 63.3 | | | | | |
| 24-Jan-09 | | Cloudy | 0.5N | 16 | 536789 | 536889 | 60.0 | 40 | 40 | 1.39 | 1.39 | 1.39 | 83.68 | 2.8428 | 2.8492 | 0.0064 | 75.5 | 78.1 | 327.4/500 | Nil | Nil | |
| | | Cloudy | 0.5N | 16 | 536889 | 536989 | 60.0 | 40 | 40 | 1.39 | 1.39 | 1.39 | 83.68 | 2.8792 | 2.8854 | 0.0062 | 74.1 | | | | | |
| | | Cloudy | 0.5N | 16 | 536989 | 537089 | 60.0 | 40 | 40 | 1.39 | 1.39 | 1.39 | 83.68 | 2.886 | 2.893 | 0.0070 | 83.7 | | | | | |
| 29-Jan-09 | | Cloudy | 0.4NE | 16 | 537089 | 537189 | 60.0 | 40 | 40 | 1.39 | 1.39 | 1.39 | 83.68 | 2.8768 | 2.8805 | 0.0037 | 44.2 | 72.9 | 327.4/500 | Nil | Nil | |
| | | Cloudy | 0.4NE | 16 | 537189 | 537289 | 60.0 | 40 | 40 | 1.39 | 1.39 | 1.39 | 83.68 | 2.8586 | 2.865 | 0.0064 | 76.5 | | | | | |
| | | Cloudy | 0.4NE | 16 | 537289 | 537389 | 60.0 | 40 | 40 | 1.39 | 1.39 | 1.39 | 83.68 | 2.8728 | 2.881 | 0.0082 | 98.0 | | | | | |
| Long Beach Gardens - Outfall (ASR8) | | 3-Jan-09 | Cloudy | 0.5E | 15 | 590693 | 590793 | 60.0 | 40 | 40 | 1.37 | 1.37 | 1.37 | 81.91 | 2.8958 | 2.891 | 0.0052 | 63.5 | 78.5 | 336.6/500 | Excavation by backhoe | Traffic |
| | | | Cloudy | 0.5E | 15 | 590793 | 590893 | 60.0 | 40 | 40 | 1.37 | 1.37 | 1.37 | 81.91 | 2.8266 | 2.8337 | 0.0071 | 88.7 | | | | |
| | | | Cloudy | 0.5E | 15 | 590893 | 590993 | 60.0 | 40 | 40 | 1.37 | 1.37 | 1.37 | 81.91 | 2.8556 | 2.8626 | 0.0070 | 85.5 | | | | |
| | | 9-Jan-09 | Sunny | 0.6NE | 16 | 590993 | 591093 | 60.0 | 40 | 40 | 1.37 | 1.37 | 1.37 | 81.91 | 2.876 | 2.8896 | 0.0136 | 166.0 | 138.8 | 336.6/500 | Excavation by backhoe | Traffic |
| | | | Sunny | 0.6NE | 16 | 591093 | 591193 | 60.0 | 40 | 40 | 1.37 | 1.37 | 1.37 | 81.91 | 2.8116 | 2.8196 | 0.0080 | 97.7 | | | | |
| | | | Sunny | 0.6NE | 16 | 591193 | 591293 | 60.0 | 40 | 40 | 1.37 | 1.37 | 1.37 | 81.91 | 2.8772 | 2.8897 | 0.0125 | 152.6 | | | | |
| | 15-Jan-09 | Sunny | 0.5NE | 16 | 591293 | 591393 | 60.0 | 40 | 40 | 1.37 | 1.37 | 1.37 | 81.91 | 2.8372 | 2.8510 | 0.0138 | 168.5 | 162.0 | 336.6/500 | Excavation by backhoe , breaking by backhoe | Traffic | |
| | | Sunny | 0.5NE | 16 | 591393 | 591493 | 60.0 | 40 | 40 | 1.37 | 1.37 | 1.37 | 81.91 | 2.8079 | 2.8211 | 0.0132 | 161.2 | | | | | |
| | | Sunny | 0.5NE | 16 | 591493 | 591593 | 60.0 | 40 | 40 | 1.37 | 1.37 | 1.37 | 81.91 | 2.8701 | 2.8829 | 0.0128 | 156.3 | | | | | |
| | 21-Jan-09 | Sunny | 0.5NE | 17 | 591593 | 591693 | 60.0 | 40 | 40 | 1.37 | 1.37 | 1.37 | 81.91 | 2.8758 | 2.8845 | 0.0087 | 106.2 | 110.7 | 336.6/500 | Excavation by backhoe , breaking by backhoe | Traffic | |
| | | Sunny | 0.5NE | 17 | 591693 | 591793 | 60.0 | 40 | 40 | 1.37 | 1.37 | 1.37 | 81.91 | 2.8841 | 2.8927 | 0.0086 | 105.0 | | | | | |
| | | Sunny | 0.5NE | 17 | 591793 | 591893 | 60.0 | 40 | 40 | 1.37 | 1.37 | 1.37 | 81.91 | 2.8250 | 2.8349 | 0.0099 | 120.9 | | | | | |
| | 24-Jan-09 | Sunny | 0.7NE | 19 | 591893 | 591993 | 60.0 | 40 | 40 | 1.37 | 1.37 | 1.37 | 81.91 | 2.8308 | 2.8406 | 0.0098 | 119.6 | 106.6 | 336.6/500 | Nil | Nil | |
| | | Sunny | 0.7NE | 19 | 591993 | 592093 | 60.0 | 40 | 40 | 1.37 | 1.37 | 1.37 | 81.91 | 2.8533 | 2.8609 | 0.0076 | 92.8 | | | | | |
| | | Sunny | 0.7NE | 19 | 592093 | 592193 | 60.0 | 40 | 40 | 1.37 | 1.37 | 1.37 | 81.91 | 2.8577 | 2.8655 | 0.0088 | 107.4 | | | | | |
| | 29-Jan-09 | Cloudy | 0.6E | 18 | 592193 | 592293 | 60.0 | 40 | 40 | 1.37 | 1.37 | 1.37 | 81.91 | 2.8476 | 2.8570 | 0.0094 | 114.8 | 117.6 | 336.6/500 | Nil | Nil | |
| | | Cloudy | 0.6E | 18 | 592293 | 592393 | 60.0 | 40 | 40 | 1.37 | 1.37 | 1.37 | 81.91 | 2.8445 | 2.8537 | 0.0092 | 112.3 | | | | | |
| | | Cloudy | 0.6E | 18 | 592393 | 592493 | 60.0 | 40 | 40 | 1.37 | 1.37 | 1.37 | 81.91 | 2.8256 | 2.8359 | 0.0103 | 125.8 | | | | | |
| | Greenview Terrace - Outfall (ASR9) | 3-Jan-09 | Cloudy | 0.9E | 15 | 522593 | 522693 | 60.0 | 40 | 40 | 1.26 | 1.26 | 1.26 | 75.69 | 2.9015 | 2.9057 | 0.0042 | 55.5 | 58.6 | 329.2/500 | Excavation by backhoe | Traffic |
| | | | Cloudy | 0.9E | 15 | 522693 | 522793 | 60.0 | 40 | 40 | 1.26 | 1.26 | 1.26 | 75.69 | 2.8523 | 2.8566 | 0.0043 | 56.8 | | | | |
| | | | Cloudy | 0.9E | 15 | 522793 | 522893 | 60.0 | 40 | 40 | 1.26 | 1.26 | 1.26 | 75.69 | 2.8493 | 2.8541 | 0.0048 | 63.4 | | | | |
| | | 9-Jan-09 | Sunny | 0.6NE | 16 | 522893 | 522993 | 60.0 | 40 | 40 | 1.26 | 1.26 | 1.26 | 75.69 | 2.8643 | 2.873 | 0.0087 | 114.9 | 94.7 | 329.2/500 | Excavation by backhoe | Traffic |
| | | | Sunny | 0.6NE | 16 | 522993 | 523093 | 60.0 | 40 | 40 | 1.26 | 1.26 | 1.26 | 75.69 | 2.8891 | 2.8939 | 0.0048 | 63.4 | | | | |
| | | | Sunny | 0.6NE | 16 | 523093 | 523193 | 60.0 | 40 | 40 | 1.26 | 1.26 | 1.26 | 75.69 | 2.8747 | 2.8827 | 0.0080 | 105.7 | | | | |
| 15-Jan-09 | | Sunny | 0.8NE | 16 | 523193 | 523293 | 60.0 | 40 | 40 | 1.26 | 1.26 | 1.26 | 75.69 | 2.8215 | 2.8301 | 0.0086 | 113.6 | 108.3 | 329.2/500 | Excavation by backhoe , breaking by backhoe | Traffic | |
| | | Sunny | 0.8NE | 16 | 523293 | 523393 | 60.0 | 40 | 40 | 1.26 | 1.26 | 1.26 | 75.69 | 2.7924 | 2.8002 | 0.0078 | 103.1 | | | | | |
| | | Sunny | 0.8NE | 16 | 523393 | | | | | | | | | | | | | | | | | |


**Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
 Air Quality Monitoring (1-hr TSP) Results at Sik Sik Yuen Ho Fung College - Intake (ASR1)
 Oct-08 to Jan-09**

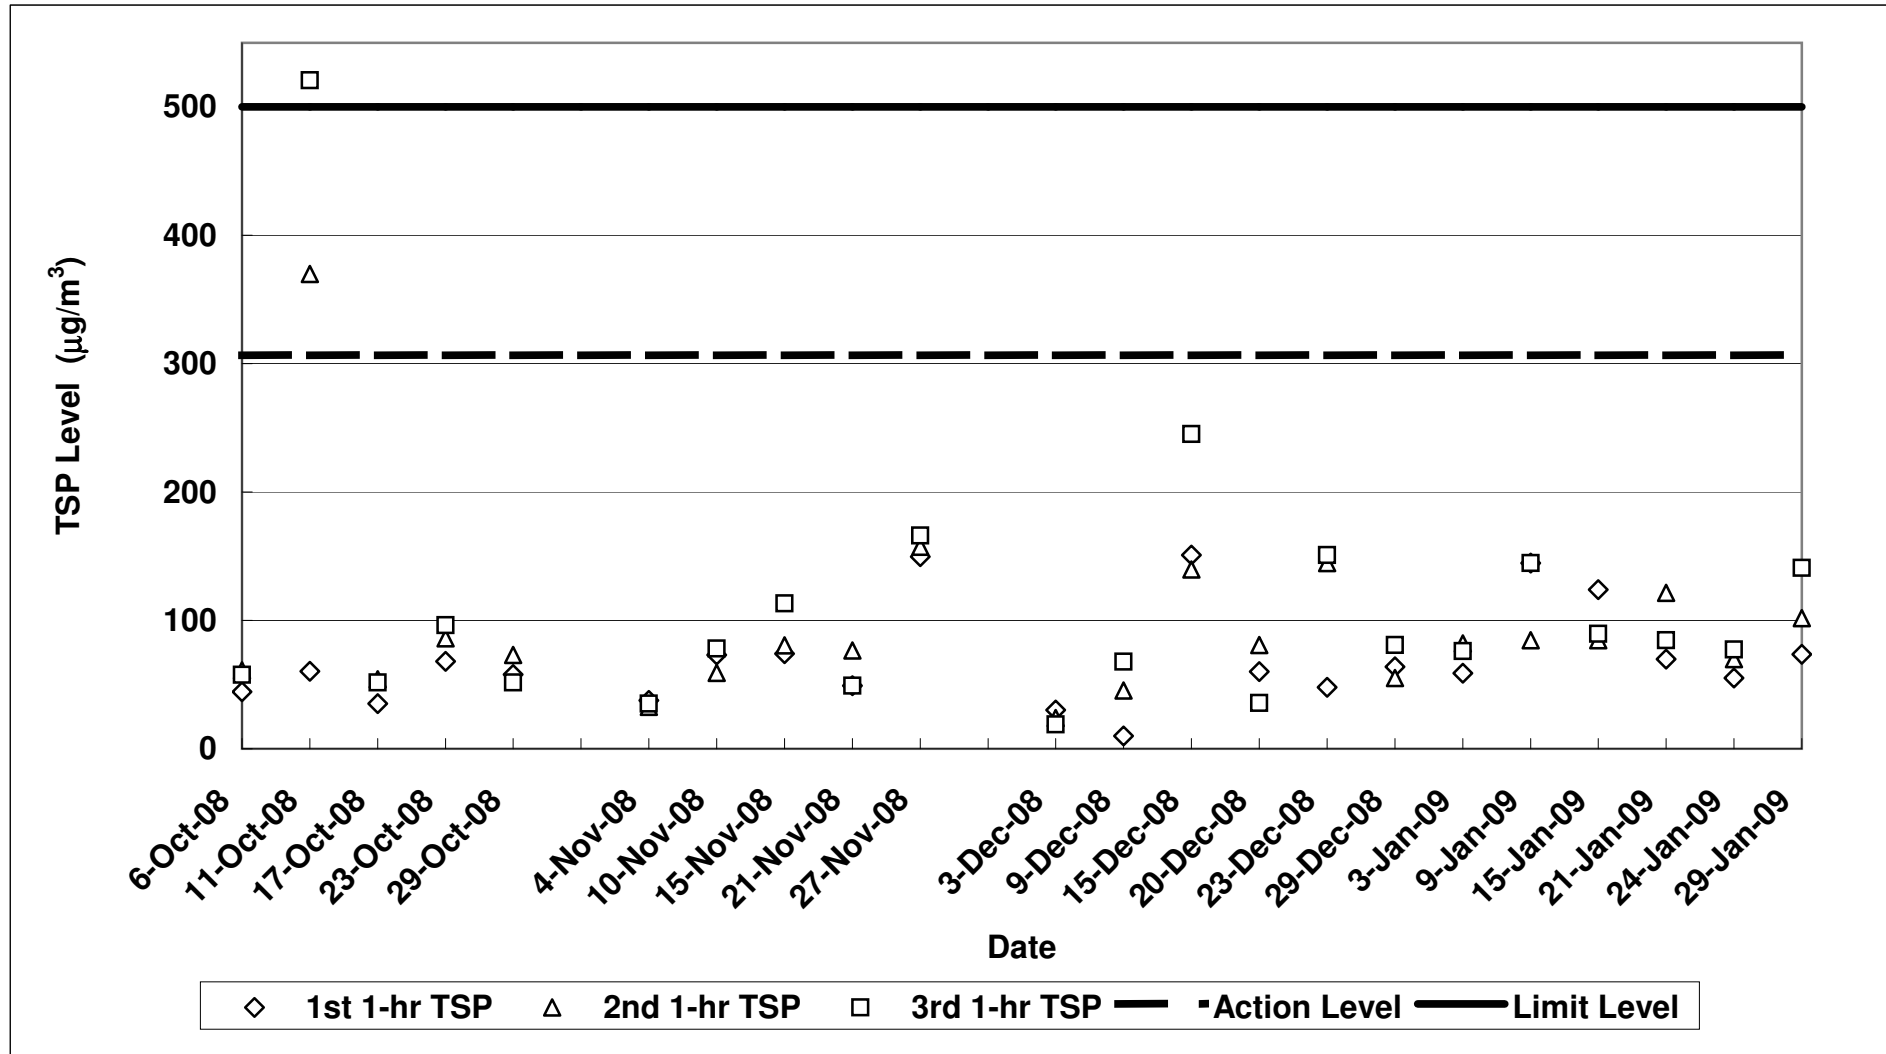


**Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
 Air Quality Monitoring (1-hr TSP) Results at Hong Hoi Chee Hong Temple - Intake (ASR3)
 Oct-08 to Jan-09**

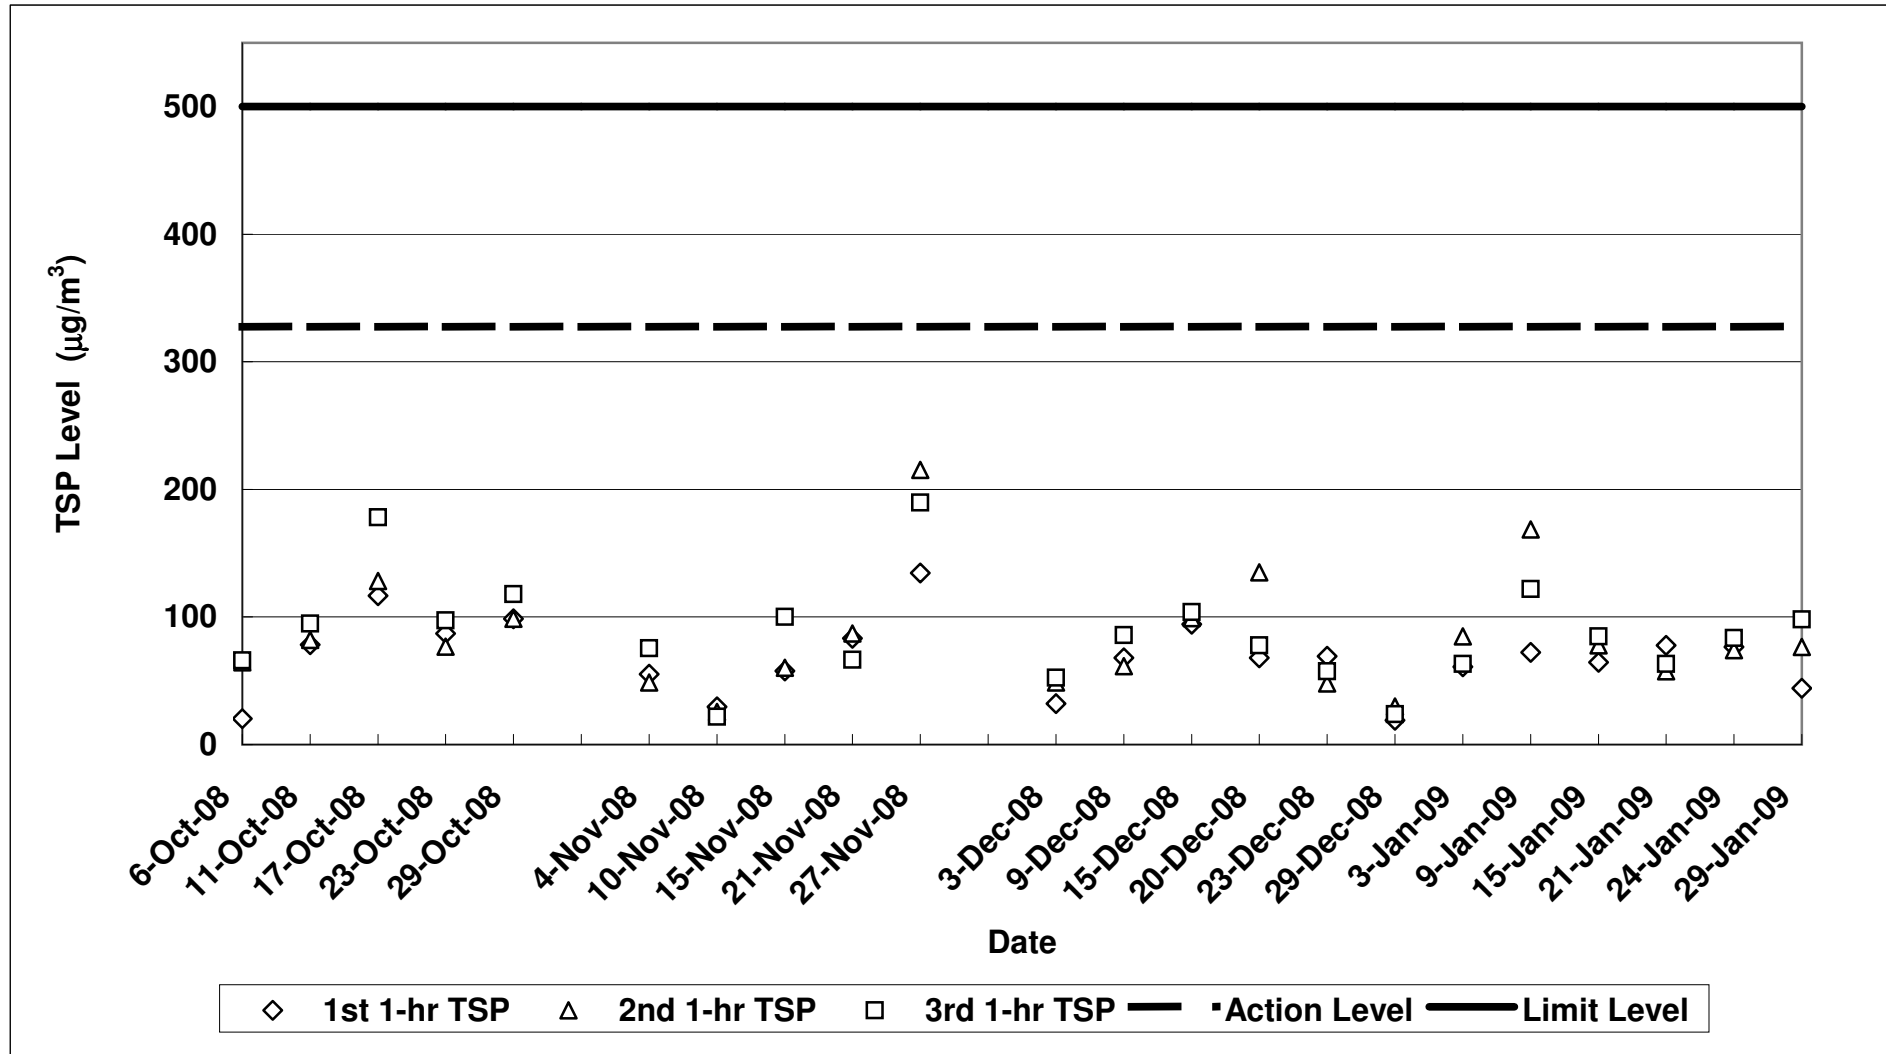

**Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
 Air Quality Monitoring (1-hr TSP) Results at Long Beach Gardens - Outfall (ASR8)
 Oct-08 to Jan-09**

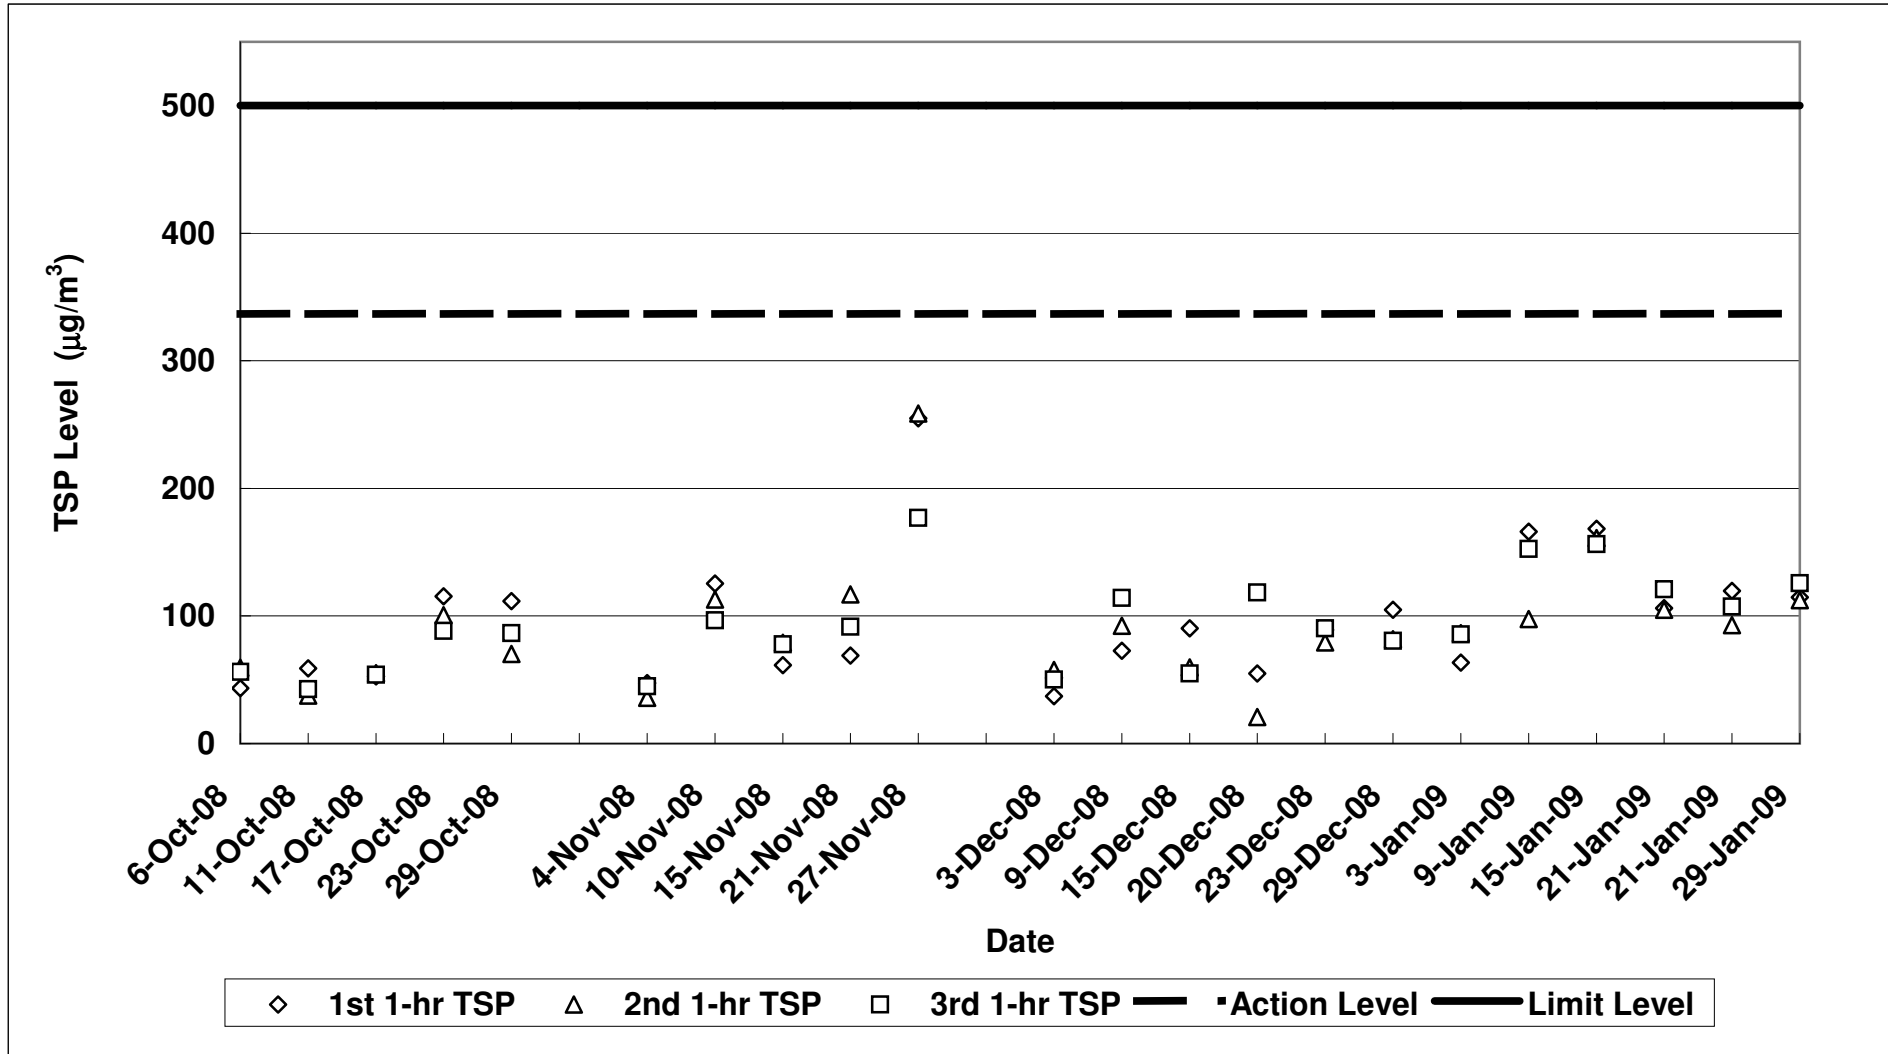

**Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
 Air Quality Monitoring (1-hr TSP) Results at Greenview Terrance - Outfall (ASR9)
 Oct-08 to Jan-09**

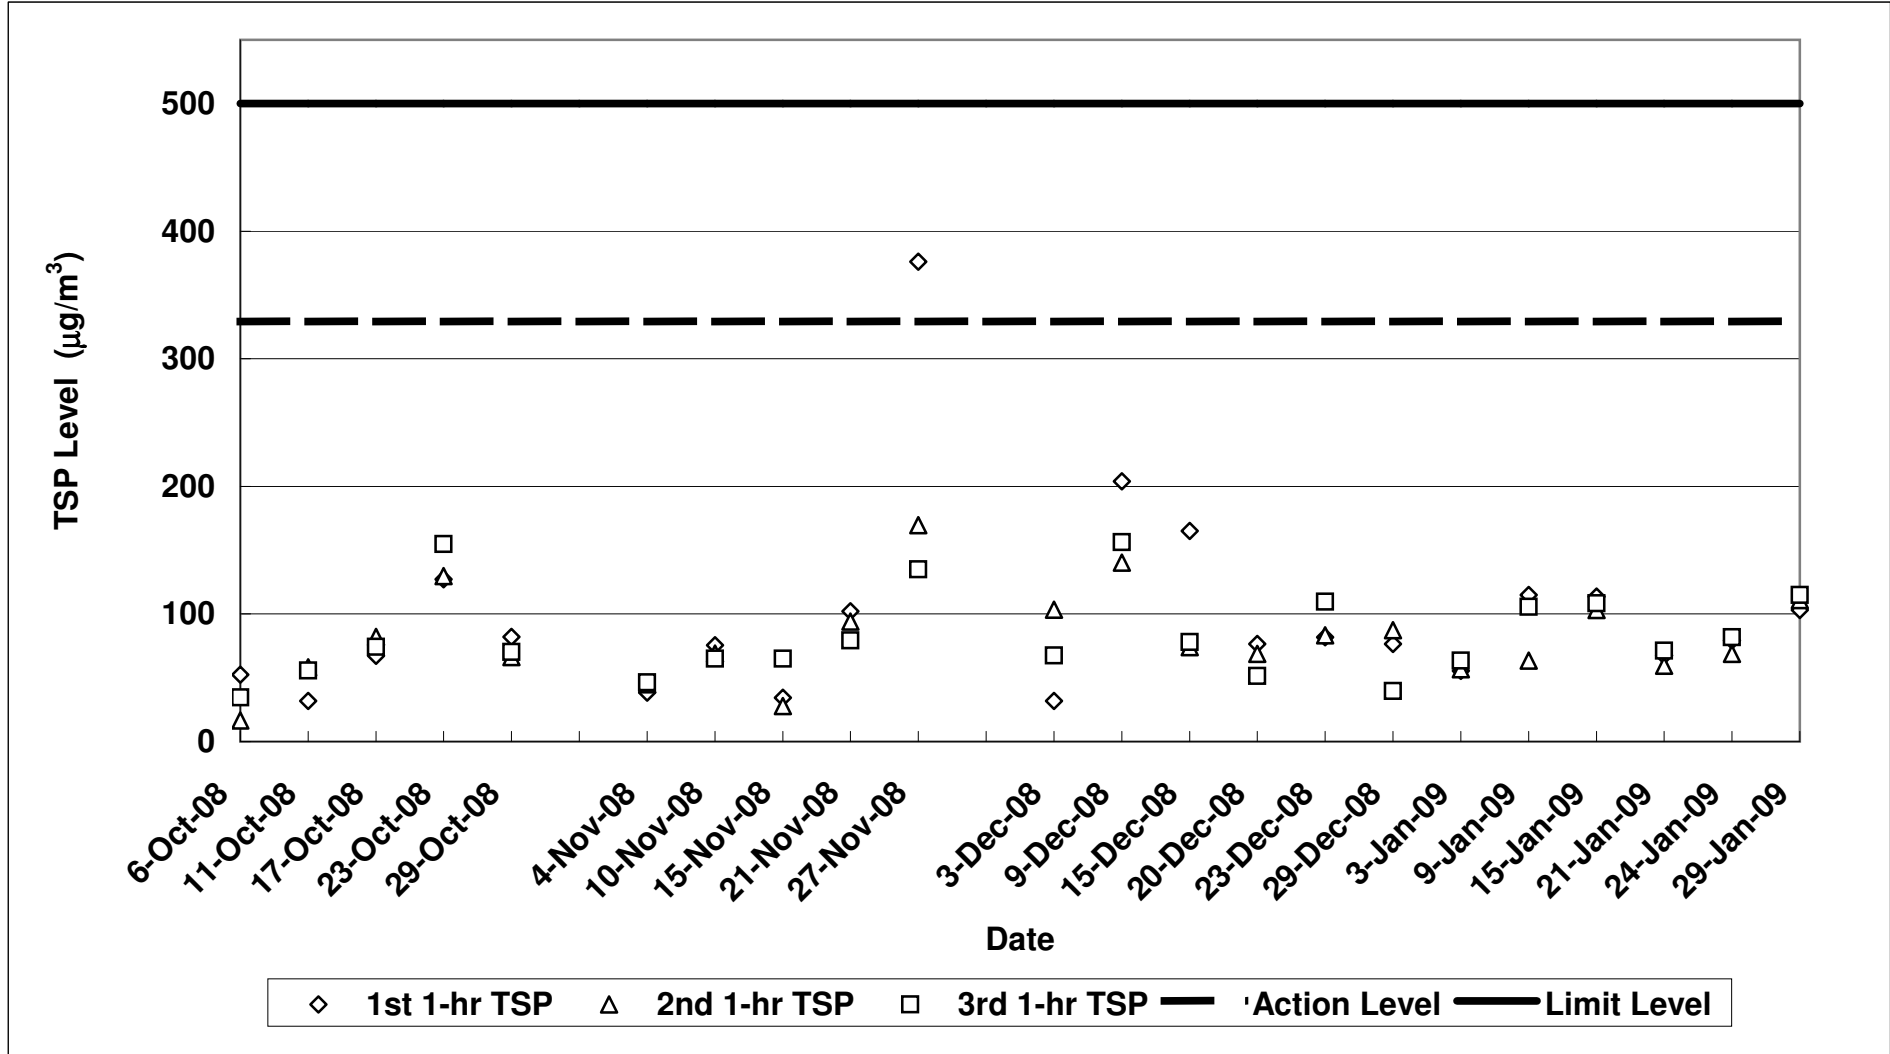

Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel

Noise Impact Monitoring Results

| Monitoring Locations | Date | Weather Conditions | Temperature (°C) | Wind Speed (m/s) | Wind Direction | Start Time | End Time | BL ¹ dB(A) | LL ² dB(A) | L _{eq} (30min) dB(A) | L ₁₀ (30min) dB(A) | L ₉₀ (30min) dB(A) | CNL ³ dB(A) | Observation / Site Condition | Remark |
|---------------------------------------|-----------|--------------------|------------------|------------------|----------------|------------|----------|-----------------------|-----------------------|-------------------------------|-------------------------------|-------------------------------|------------------------|---|-------------------------------|
| | | | | | | | | | | | | | | | |
| Sik Sik Yuen Ho Fung College NSR 1 | 9-Jan-09 | Sunny | 12 | 0.7 | E | 8:30 | 9:00 | 66.1 | 70 | 61.5 | 64.8 | 57.8 | - | Site tidiness | Traffic noise |
| | 16-Jan-09 | Sunny | 14 | 0.6 | NE | 11:30 | 12:00 | | 70 | 62.5 | 65.4 | 57.9 | - | Nil | Traffic noise, human activity |
| | 21-Jan-09 | Sunny | 23 | 0.7 | NE | 16:38 | 17:08 | | 70 | 64.5 | 67.5 | 59.9 | - | Nil | Traffic noise |
| | 29-Jan-09 | Cloudy | 15 | 0.5 | NE | 11:30 | 12:00 | | 70 | 63.0 | 65.8 | 60.3 | - | Nil | Traffic noise |
| | - | - | - | - | - | - | - | | - | - | - | - | - | - | - |
| Hong Hoi Chee Hong Temple NSR 3 | 9-Jan-09 | Sunny | 12 | 0.6 | N | 11:30 | 12:00 | 57.9 | 75 | 71.1 | 72.9 | 68.1 | - | Piling | Nil |
| | 16-Jan-09 | Sunny | 14 | 0.5 | NE | 11:30 | 12:00 | | 75 | 71.4 | 74.3 | 68.4 | - | Piling | Traffic noise |
| | 21-Jan-09 | Sunny | 18 | 0.4 | NE | 11:30 | 12:00 | | 75 | 66.1 | 69.1 | 63.0 | - | Piling | Traffic noise , water fall |
| | 29-Jan-09 | Cloudy | 15 | 0.4 | NE | 11:30 | 12:00 | | 75 | 60.0 | 62.8 | 56.7 | - | Nil | Traffic noise |
| | - | - | - | - | - | - | - | | - | - | - | - | - | - | - |
| Squatters NSR 6 | 9-Jan-09 | Sunny | 12 | 0.6 | N | 13:05 | 13:35 | 61.2 | 75 | 63.6 | 66.4 | 60.5 | - | Nil | Dog Darking |
| | 16-Jan-09 | Sunny | 15 | 0.3 | NE | 13:05 | 13:35 | | 75 | 63.7 | 66.7 | 60.7 | - | Nil | Dog Darking |
| | 21-Jan-09 | Sunny | 22 | 0.4 | NE | 15:30 | 16:00 | | 75 | 65.7 | 67.4 | 63.1 | - | Nil | Dog Darking |
| | 29-Jan-09 | Cloudy | 18 | 0.3 | NE | 15:15 | 15:45 | | 75 | 59.5 | 62.6 | 56.5 | - | Nil | Nil |
| | - | - | - | - | - | - | - | | - | - | - | - | - | - | - |
| Long Beach Gardens NSR 8 | 9-Jan-09 | Sunny | 15 | 0.6 | NE | 13:50 | 14:20 | 60.9 | 75 | 64.2 | 67.3 | 58.9 | - | Excavation by backhoe | Traffic noise |
| | 16-Jan-09 | Sunny | 16 | 0.5 | NE | 13:00 | 13:30 | | 75 | 64.7 | 67.0 | 60.7 | - | Nil | Traffic noise |
| | 21-Jan-09 | Sunny | 18 | 0.5 | NE | 9:20 | 9:50 | | 75 | 64.6 | 68.8 | 58.4 | - | Excavation by backhoe , breaking by backhoe | Traffic noise |
| | 29-Jan-09 | Cloudy | 18 | 0.6 | E | 14:25 | 14:55 | | 75 | 58.8 | 60.6 | 56.5 | - | Nil | Traffic noise |
| | - | - | - | - | - | - | - | | - | - | - | - | - | - | - |
| Greenview Terrace NSR 9 | 9-Jan-09 | Sunny | 15 | 0.6 | NE | 14:50 | 15:20 | 59.7 | 75 | 61.4 | 64.3 | 57.6 | - | Excavation by backhoe | Traffic noise |
| | 16-Jan-09 | Sunny | 16 | 0.8 | NE | 14:55 | 15:25 | | 75 | 66.7 | 69.0 | 62.3 | - | Excavation by backhoe , breaking by backhoe | Traffic noise |
| | 21-Jan-09 | Sunny | 18 | 0.4 | NE | 10:20 | 10:50 | | 75 | 66.0 | 68.6 | 63.1 | - | Excavation by backhoe , breaking by backhoe | Traffic noise |
| | 29-Jan-09 | Cloudy | 18 | 1 | E | 15:25 | 15:55 | | 75 | 51.9 | 53.6 | 50.0 | - | Nil | Traffic noise |
| | - | - | - | - | - | - | - | | - | - | - | - | - | - | - |

1: Baseline Noise Level

2: Limit Level


3: Corrected Noise Level

Note:


The limit level of NSR1 is 65dB(A) during school examination period.

Red Bold indicates an exceedance of Limit Level


**Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
 Noise Monitoring Results at Sik Sik Yuen Ho Fung College (NSR 1)
 Oct-08 to Jan-09**

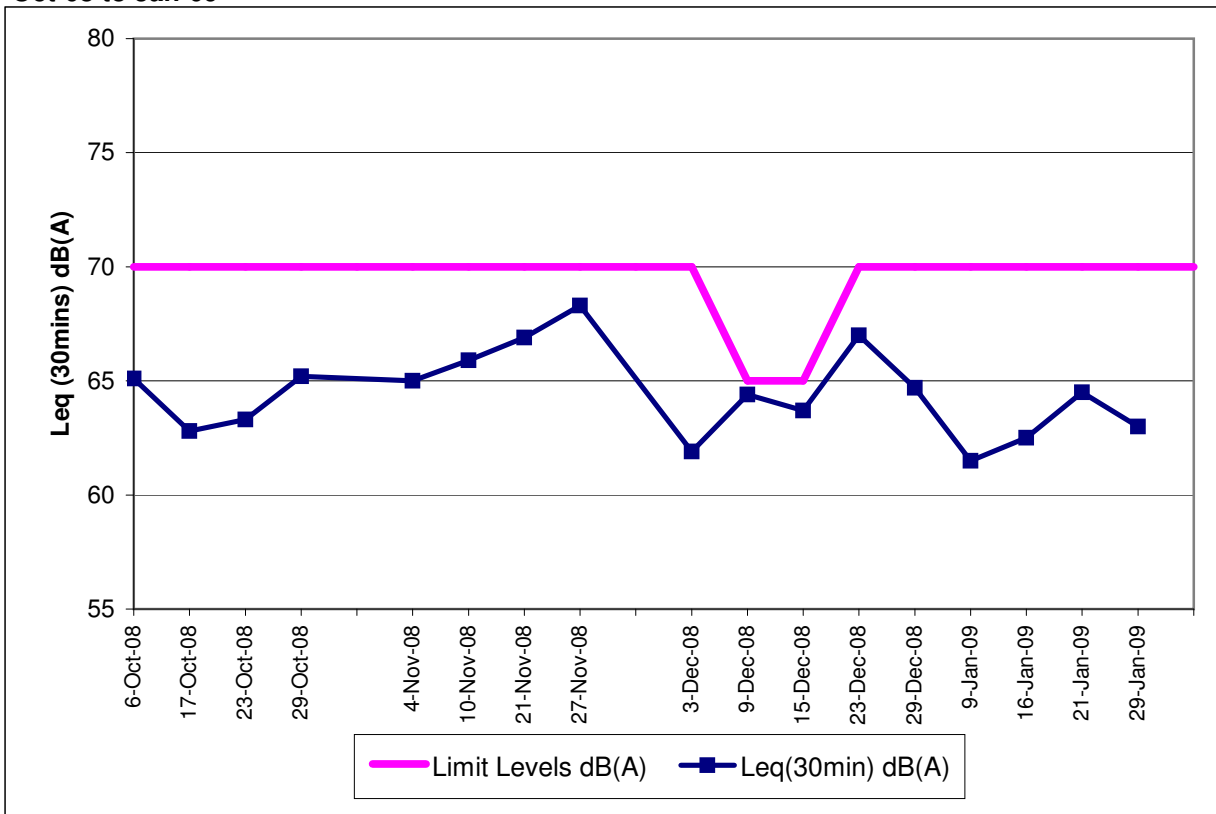


**Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
 Noise Monitoring Results at Hong Hoi Chee Hong Temple (NSR 3)
 Oct-08 to Jan-09**

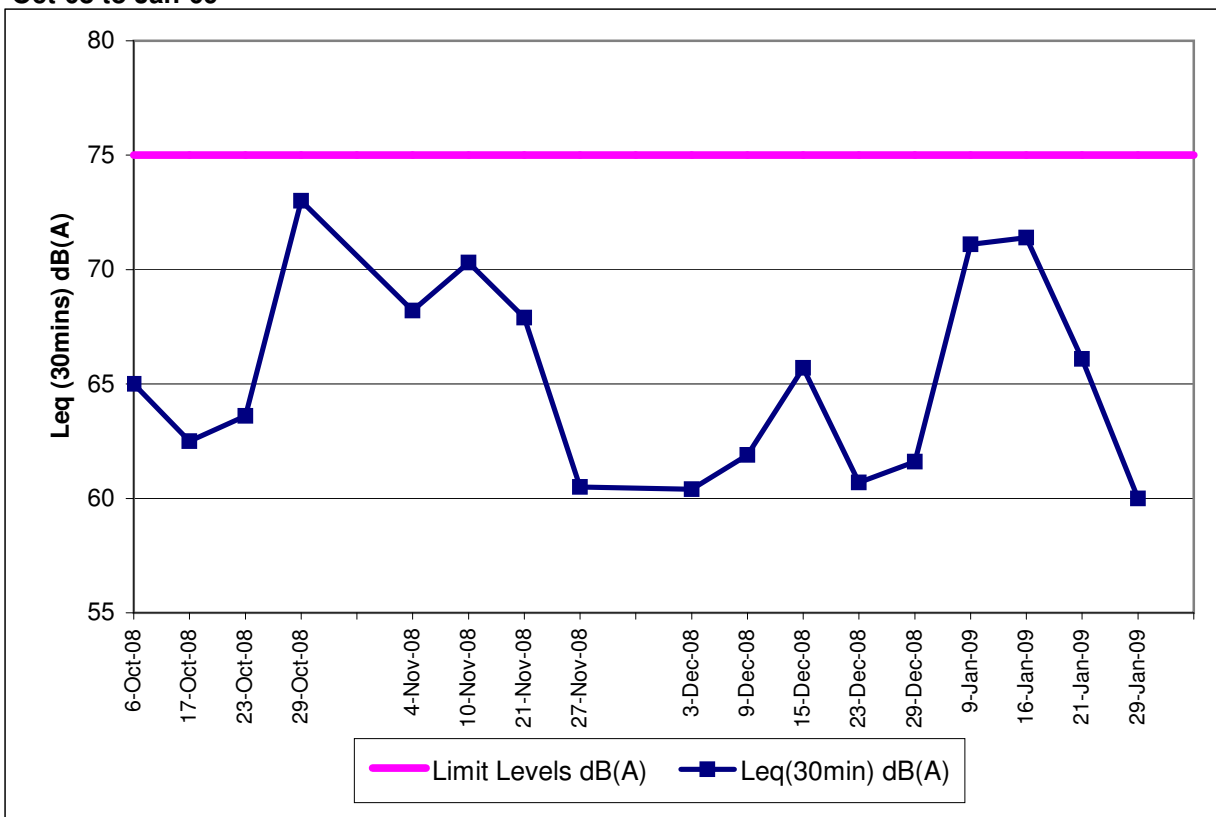


**Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
 Noise Monitoring Results at Squatters (NSR 6)
 Oct-08 to Jan-09**

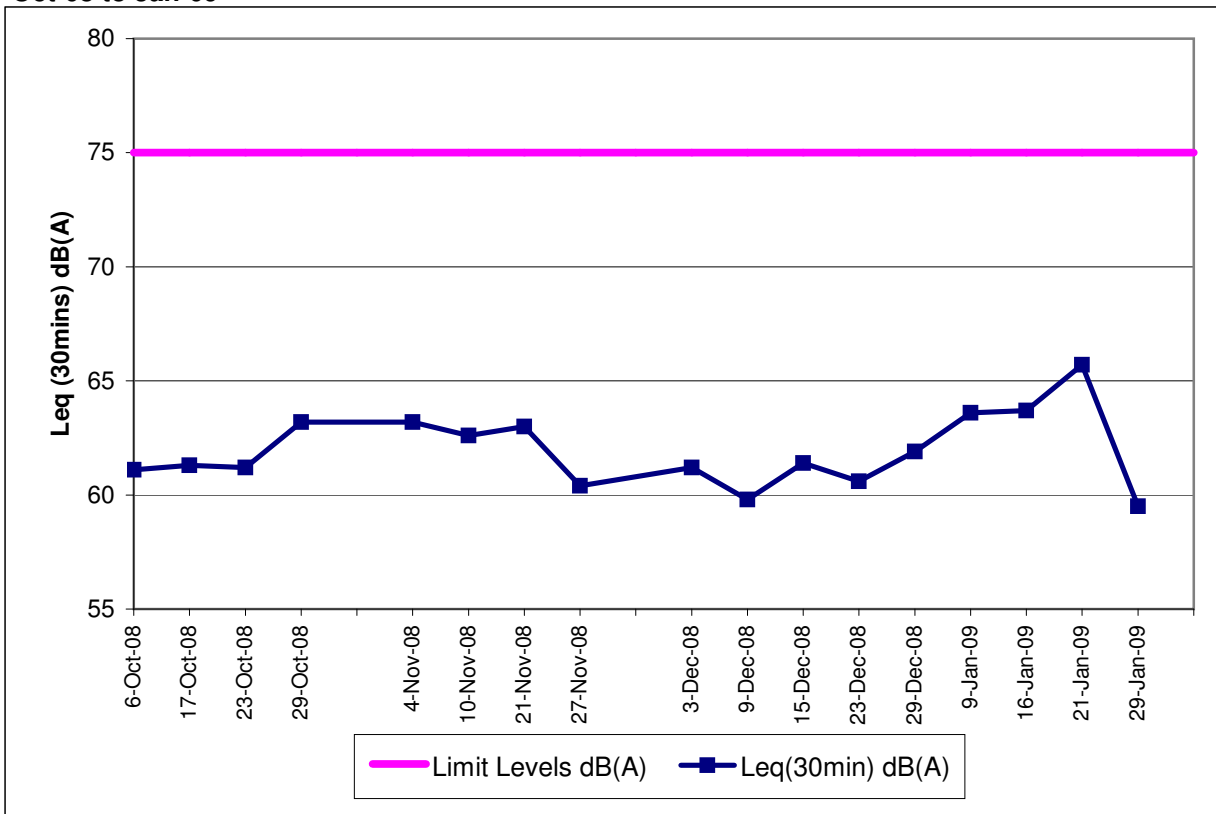

**Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
 Noise Monitoring Results at Long Beach Gardens (NSR 8)
 Oct-08 to Jan-09**

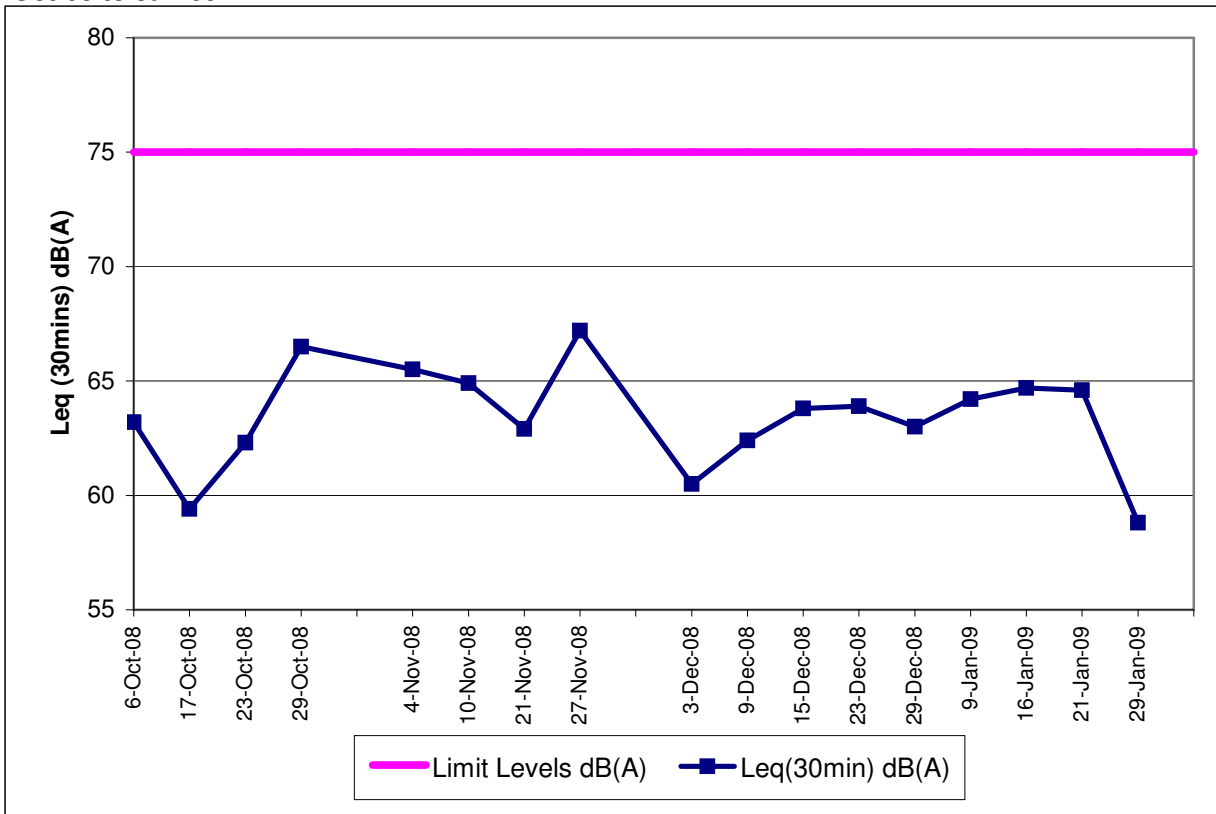

**Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Noise Monitoring Results at Greenview Terrace (NSR 9)
Oct-08 to Jan-09**

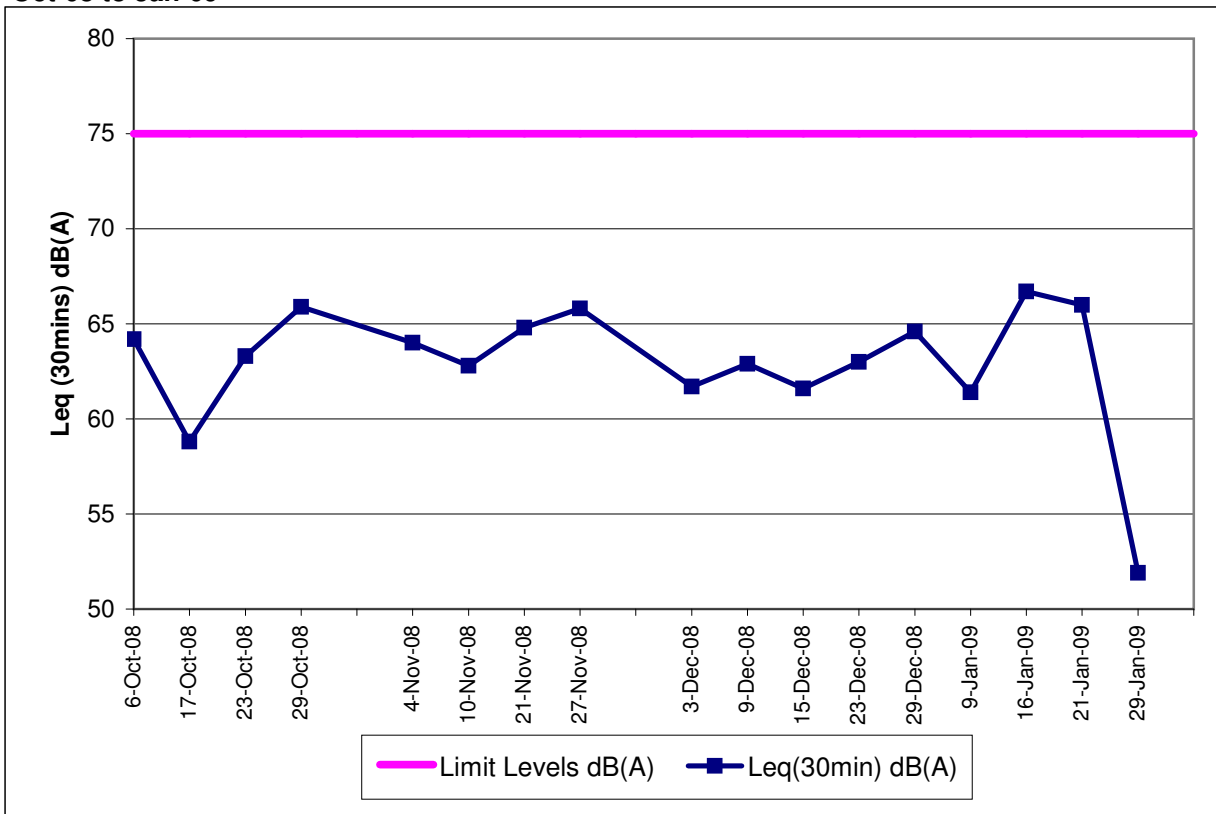


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel


Water Quality Impact Monitoring Results

| Monitoring Locations | Date | Start Time | Weather | Water Depth(m) | Temp | | | DO(mg/L) | | | Action/Limit Level of DO(mg/L) | pH | | | Turbidity(NTU) | | | Action/Limit Level of Tby | SS (mg/L) | | | Action/Limit Level of SS(mg/L) | Remarks: | Action to be taken |
|----------------------------------|------------------------------------|------------|---------|----------------|-------|-------|-------|----------|------|------|--------------------------------|------|------|------|----------------|------|------|---------------------------|-----------|-----------------------|---------------------------------------|--------------------------------|----------|--------------------|
| | | | | | 1 | 2 | Avg | 1 | 2 | Avg | | 1 | 2 | Avg | 1 | 2 | Avg | | 1 | 2 | Avg | | | |
| Sik Sik Yuen Ho Fung College I-1 | 2-Jan-09 | 9:05 | Sunny | <1 | 18.50 | 18.50 | 18.50 | 4.77 | 4.75 | 4.76 | 7.77 | 7.77 | 7.77 | 4.18 | 4.15 | 4.17 | 2.0 | 2.0 | 2.0 | Nil | | | | |
| | 5-Jan-09 | 9:50 | Sunny | <1 | 18.20 | 18.20 | 18.20 | 4.85 | 4.88 | 4.87 | 7.22 | 7.22 | 7.22 | 3.73 | 3.70 | 3.72 | 2.0 | 2.0 | 2.0 | Nil | | | | |
| | 7-Jan-09 | 9:35 | Sunny | <1 | 18.30 | 18.30 | 18.30 | 4.43 | 4.42 | 4.43 | 7.75 | 7.75 | 7.75 | 4.18 | 4.22 | 4.20 | 2.0 | 2.0 | 2.0 | Excavation by backhoe | | | | |
| | 9-Jan-09 | 9:20 | Sunny | <1 | 18.10 | 18.20 | 18.15 | 4.22 | 4.27 | 4.25 | 7.75 | 7.76 | 7.76 | 4.01 | 4.02 | 4.02 | 4.2 | 3.9 | 4.1 | Nil | | | | |
| | 12-Jan-09 | 9:45 | Sunny | <1 | 15.30 | 15.20 | 15.25 | 5.72 | 5.75 | 5.74 | 7.55 | 7.55 | 7.55 | 5.44 | 5.42 | 5.43 | 2.0 | 2.0 | 2.0 | Nil | | | | |
| | 14-Jan-09 | 9:38 | Sunny | <1 | 18.50 | 18.50 | 18.50 | 4.82 | 4.83 | 4.83 | 7.55 | 7.53 | 7.54 | 4.68 | 4.62 | 4.65 | 4.0 | 4.1 | 4.1 | Nil | | | | |
| | 16-Jan-09 | 9:38 | Sunny | <1 | 15.40 | 15.40 | 15.40 | 5.33 | 5.30 | 5.32 | 7.43 | 7.43 | 7.43 | 5.07 | 5.10 | 5.09 | 2.0 | 2.0 | 2.0 | Nil | | | | |
| | 19-Jan-09 | 9:38 | Sunny | <1 | 17.80 | 17.80 | 17.80 | 4.52 | 4.54 | 4.53 | 7.73 | 7.75 | 7.74 | 5.22 | 5.19 | 5.21 | 2.0 | 2.0 | 2.0 | Nil | | | | |
| | 21-Jan-09 | 13:48 | Sunny | <1 | 17.50 | 17.50 | 17.50 | 5.87 | 5.86 | 5.87 | 7.52 | 7.51 | 7.52 | 4.22 | 4.24 | 4.23 | 2.0 | 2.0 | 2.0 | Nil | | | | |
| | 23-Jan-09 | 9:36 | Sunny | <1 | 16.50 | 16.50 | 16.50 | 5.52 | 5.57 | 5.55 | 7.71 | 7.71 | 7.71 | 5.16 | 5.13 | 5.15 | 2.0 | 2.0 | 2.0 | Nil | | | | |
| | 29-Jan-09 | 13:35 | Cloudy | <1 | 16.00 | 16.00 | 16.00 | 6.46 | 6.45 | 6.46 | 7.73 | 7.73 | 7.73 | 5.32 | 5.38 | 5.35 | 3.7 | 3.5 | 3.6 | Nil | | | | |
| | 31-Jan-09 | 9:22 | Sunny | <1 | 17.30 | 17.30 | 17.30 | 6.22 | 6.27 | 6.25 | 8.03 | 8.03 | 8.03 | 5.15 | 5.11 | 5.13 | 3.7 | 4.2 | 4.0 | Nil | | | | |
| | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | |
| | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| | Sik Sik Yuen Ho Fung College I-1-C | 2-Jan-09 | 9:36 | Sunny | <1 | 18.80 | 18.80 | 18.80 | 4.67 | 4.65 | 4.66 | 7.72 | 7.72 | 7.72 | 4.21 | 4.22 | 4.22 | 2.0 | 2.0 | 2.0 | Nil | | | |
| | | 5-Jan-09 | 9:29 | Sunny | <1 | 18.00 | 18.00 | 18.00 | 4.90 | 4.93 | 4.92 | 7.22 | 7.20 | 7.21 | 3.86 | 3.89 | 3.88 | 2.0 | 2.0 | 2.0 | Nil | | | |
| 7-Jan-09 | | 9:20 | Sunny | <1 | 18.20 | 18.20 | 18.20 | 4.95 | 4.92 | 4.94 | 7.77 | 7.77 | 7.77 | 4.23 | 4.35 | 4.29 | 2.0 | 2.0 | 2.0 | Nil | | | | |
| 9-Jan-09 | | 9:00 | Sunny | <1 | 18.20 | 18.00 | 18.10 | 4.19 | 4.17 | 4.18 | 7.72 | 7.74 | 7.73 | 3.96 | 3.98 | 3.97 | 3.6 | 4.2 | 3.9 | Nil | | | | |
| 12-Jan-09 | | 9:15 | Sunny | <1 | 15.30 | 15.30 | 15.30 | 5.84 | 5.86 | 5.85 | 7.53 | 7.53 | 7.53 | 5.47 | 5.46 | 5.47 | 2.0 | 2.0 | 2.0 | Nil | | | | |
| 14-Jan-09 | | 9:13 | Sunny | <1 | 18.20 | 18.20 | 18.20 | 4.90 | 4.93 | 4.92 | 7.56 | 7.56 | 7.56 | 4.72 | 4.74 | 4.73 | 3.8 | 4.1 | 4.0 | Nil | | | | |
| 16-Jan-09 | | 9:17 | Sunny | <1 | 15.80 | 15.80 | 15.80 | 5.46 | 5.43 | 5.45 | 7.42 | 7.42 | 7.42 | 5.12 | 5.18 | 5.15 | 2.0 | 2.0 | 2.0 | Nil | | | | |
| 19-Jan-09 | | 9:15 | Sunny | <1 | 17.70 | 17.70 | 17.70 | 4.62 | 4.64 | 4.63 | 7.55 | 7.53 | 7.54 | 5.31 | 5.22 | 5.27 | 2.0 | 2.0 | 2.0 | Nil | | | | |
| 21-Jan-09 | | 13:20 | Sunny | <1 | 17.70 | 17.70 | 17.70 | 5.55 | 5.42 | 5.49 | 7.21 | 7.22 | 7.22 | 4.32 | 4.53 | 4.43 | 2.0 | 2.0 | 2.0 | Nil | | | | |
| 23-Jan-09 | | 9:15 | Sunny | <1 | 16.50 | 16.50 | 16.50 | 5.41 | 5.43 | 5.42 | 7.73 | 7.73 | 7.73 | 5.24 | 5.30 | 5.27 | 2.0 | 2.0 | 2.0 | Nil | | | | |
| 29-Jan-09 | | 13:09 | Cloudy | <1 | 16.00 | 16.00 | 16.00 | 6.53 | 6.53 | 6.53 | 7.71 | 7.71 | 7.71 | 5.44 | 5.46 | 5.45 | 3.9 | 4.2 | 4.1 | Nil | | | | |
| 31-Jan-09 | | 9:15 | Sunny | <1 | 17.20 | 17.20 | 17.20 | 6.34 | 6.32 | 6.33 | 8.01 | 8.12 | 8.07 | 5.26 | 5.24 | 5.25 | 5.3 | 5.6 | 5.5 | Nil | | | | |
| - | | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| - | | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| - | | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| Hong Hoi Chee Hong Temple I-2 | | 2-Jan-09 | 10:36 | Sunny | <1 | 18.30 | 18.30 | 18.30 | 4.74 | 4.73 | 4.74 | 7.73 | 7.73 | 7.73 | 5.21 | 5.27 | 5.24 | 2.0 | 2.0 | 2.0 | Piling setting | Nil | | |
| | | 5-Jan-09 | 10:55 | Sunny | <1 | 18.50 | 18.50 | 18.50 | 4.53 | 4.56 | 4.55 | 7.40 | 7.40 | 7.40 | 5.18 | 5.27 | 5.23 | 2.0 | 2.0 | 2.0 | Piling setting, excavation by backhoe | Nil | | |
| | 7-Jan-09 | 10:50 | Sunny | <1 | 17.80 | 17.80 | 17.80 | 4.69 | 4.72 | 4.71 | 7.44 | 7.44 | 7.44 | 3.70 | 3.68 | 3.69 | 2.0 | 2.0 | 2.0 | Piling setting | Nil | | | |
| | 9-Jan-09 | 10:20 | Sunny | <1 | 17.30 | 17.30 | 17.30 | 4.64 | 4.67 | 4.66 | 7.26 | 7.24 | 7.25 | 3.85 | 3.85 | 3.85 | 4.9 | 5.5 | 5.2 | Piling setting | Nil | | | |
| | 12-Jan-09 | 10:40 | Sunny | <1 | 15.00 | 15.00 | 15.00 | 5.52 | 5.57 | 5.55 | 7.43 | 7.43 | 7.43 | 4.67 | 4.65 | 4.66 | 2.0 | 2.0 | 2.0 | Piling setting | Nil | | | |
| | 14-Jan-09 | 10:36 | Sunny | <1 | 14.30 | 14.30 | 14.30 | 5.26 | 5.28 | 5.27 | 7.63 | 7.62 | 7.63 | 4.10 | 4.08 | 4.09 | 2.8 | 2.8 | 2.8 | Piling setting | Nil | | | |
| | 16-Jan-09 | 10:35 | Sunny | <1 | 15.30 | 15.20 | 15.25 | 4.80 | 4.85 | 4.83 | 7.32 | 7.33 | 7.33 | 4.33 | 4.38 | 4.36 | 2.0 | 2.0 | 2.0 | Piling setting | Nil | | | |
| | 19-Jan-09 | 11:46 | Sunny | <1 | 19.70 | 19.70 | 19.70 | 4.16 | 4.19 | 4.18 | 7.55 | 7.55 | 7.55 | 5.24 | 5.22 | 5.23 | 2.0 | 2.0 | 2.0 | Piling setting | Nil | | | |
| | 21-Jan-09 | 10:50 | Sunny | <1 | 17.70 | 17.70 | 17.70 | 4.61 | 4.52 | 4.57 | 7.55 | 7.55 | 7.55 | 4.27 | 4.20 | 4.24 | 2.0 | 2.0 | 2.0 | Piling | Nil | | | |
| | 23-Jan-09 | 10:37 | Sunny | <1 | 16.50 | 16.50 | 16.50 | 5.25 | 5.21 | 5.23 | 7.70 | 7.70 | 7.70 | 5.16 | 5.14 | 5.15 | 2.0 | 2.0 | 2.0 | Nil | | | | |
| | 29-Jan-09 | 10:48 | Cloudy | <1 | 16.00 | 16.00 | 16.00 | 6.34 | 6.31 | 6.33 | 7.72 | 7.72 | 7.72 | 5.22 | 5.24 | 5.23 | 3.7 | 3.6 | 3.7 | Nil | | | | |
| | 31-Jan-09 | 10:52 | Sunny | <1 | 17.20 | 17.20 | 17.20 | 6.38 | 6.38 | 6.38 | 7.82 | 7.82 | 7.82 | 5.42 | 5.47 | 5.45 | 2.0 | 2.0 | 2.0 | Nil | | | | |
| | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| | Hong Hoi Chee Hong Temple I-2-C | 2-Jan-09 | 10:50 | Sunny | <1 | 18.50 | 18.50 | 18.50 | 4.75 | 4.73 | 4.74 | 7.42 | 7.44 | 7.43 | 5.32 | 5.33 | 5.33 | 2.0 | 2.0 | 2.0 | Nil | | | |
| | | 5-Jan-09 | 10:35 | Sunny | <1 | 18.20 | 18.30 | 18.25 | 4.68 | 4.71 | 4.70 | 7.43 | 7.43 | 7.43 | 5.22 | 5.31 | 5.27 | 2.0 | 2.0 | 2.0 | Nil | | | |
| 7-Jan-09 | | 10:35 | Sunny | <1 | 18.00 | 18.00 | 18.00 | 4.65 | 4.68 | 4.67 | 7.43 | 7.43 | 7.43 | 3.77 | 3.86 | 3.82 | 2.0 | 2.0 | 2.0 | Nil | | | | |
| 9-Jan-09 | | 10:00 | Sunny | <1 | 17.40 | 17.30 | 17.35 | 4.77 | 4.73 | 4.75 | 7.23 | 7.25 | 7.24 | 3.82 | 3.84 | 3.83 | 3.6 | 4.8 | 4.2 | Nil | | | | |
| 12-Jan-09 | | 10:11 | Sunny | <1 | 15.20 | 15.20 | 15.20 | 5.62 | 5.58 | 5.60 | 7.44 | 7.45 | 7.45 | 4.77 | 4.72 | 4.75 | 2.0 | 2.0 | 2.0 | Nil | | | | |
| 14-Jan-09 | | 10:16 | Sunny | <1 | 14.50 | 14.30 | 14.40 | 5.32 | 5.38 | 5.35 | 7.56 | 7.56 | 7.56 | 4.12 | 4.12 | 4.12 | 2.8 | 3.0 | 2.9 | Nil | | | | |
| 16-Jan-09 | | 10:20 | Sunny | <1 | 15.80 | 15.80 | 15.80 | 4.73 | 4.76 | 4.75 | 7.33 | 7.33 | 7.33 | 4.28 | 4.30 | 4.29 | 2.0 | 2.0 | 2.0 | Nil | | | | |
| 19-Jan-09 | | 10:20 | Sunny | <1 | 19.60 | 19.60 | 19.60 | 4.04 | 4.07 | 4.06 | 7.56 | 7.56 | 7.56 | 5.35 | 5.33 | 5.34 | 2.0 | 2.0 | 2.0 | Nil | | | | |
| 21-Jan-09 | | 11:15 | Sunny | <1 | 17.50 | 17.50 | 17.50 | 4.48 | 4.52 | 4.50 | 7.72 | 7.72 | 7.72 | 4.18 | 4.22 | 4.20 | 2.0 | 2.0 | 2.0 | Piling | Nil | | | |
| 23-Jan-09 | | 10:16 | Sunny | <1 | 16.30 | 16.30 | 16.30 | 5.31 | 5.33 | 5.32 | 7.71 | 7.71 | 7.71 | 5.21 | 5.17 | 5.19 | 2.0 | 2.0 | 2.0 | Nil | | | | |
| 29-Jan-09 | | 10:15 | Cloudy | <1 | 16.20 | 16.20 | 16.20 | 6.40 | 6.38 | 6.39 | 7.71 | 7.71 | 7.71 | 5.30 | 5.28 | 5.29 | 4.0 | 3.6 | 3.8 | Nil | | | | |
| 31-Jan-09 | | 10:15 | Sunny | <1 | 17.20 | 17.20 | 17.20 | 6.23 | 6.19 | 6.21 | 7.82 | 7.82 | 7.82 | 5.63 | 5.66 | 5.65 | 2.0 | 2.0 | 2.0 | Nil | | | | |
| - | | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| - | | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| - | | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - | - |
| Squatters I-3 | | 2-Jan-09 | 11:35 | Sunny | | | | | | | | | | | | | | | | | | | | |


**Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
 Water Quality Results at Sik Sik Yuen Ho Fung College (I-1)
 Oct-08 to Jan-09**

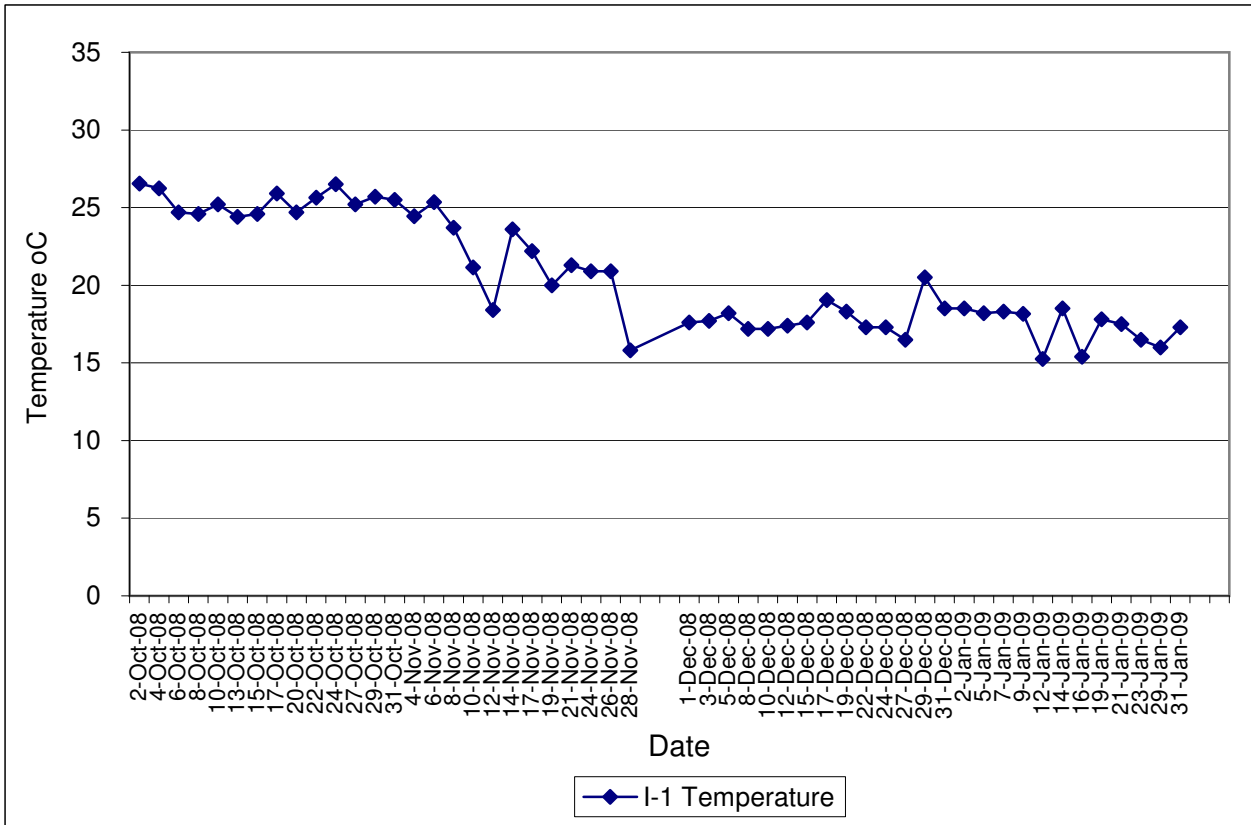


**Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
 Water Quality Results at Sik Sik Yuen Ho Fung College (I-1-C)
 Oct-08 to Jan-09**

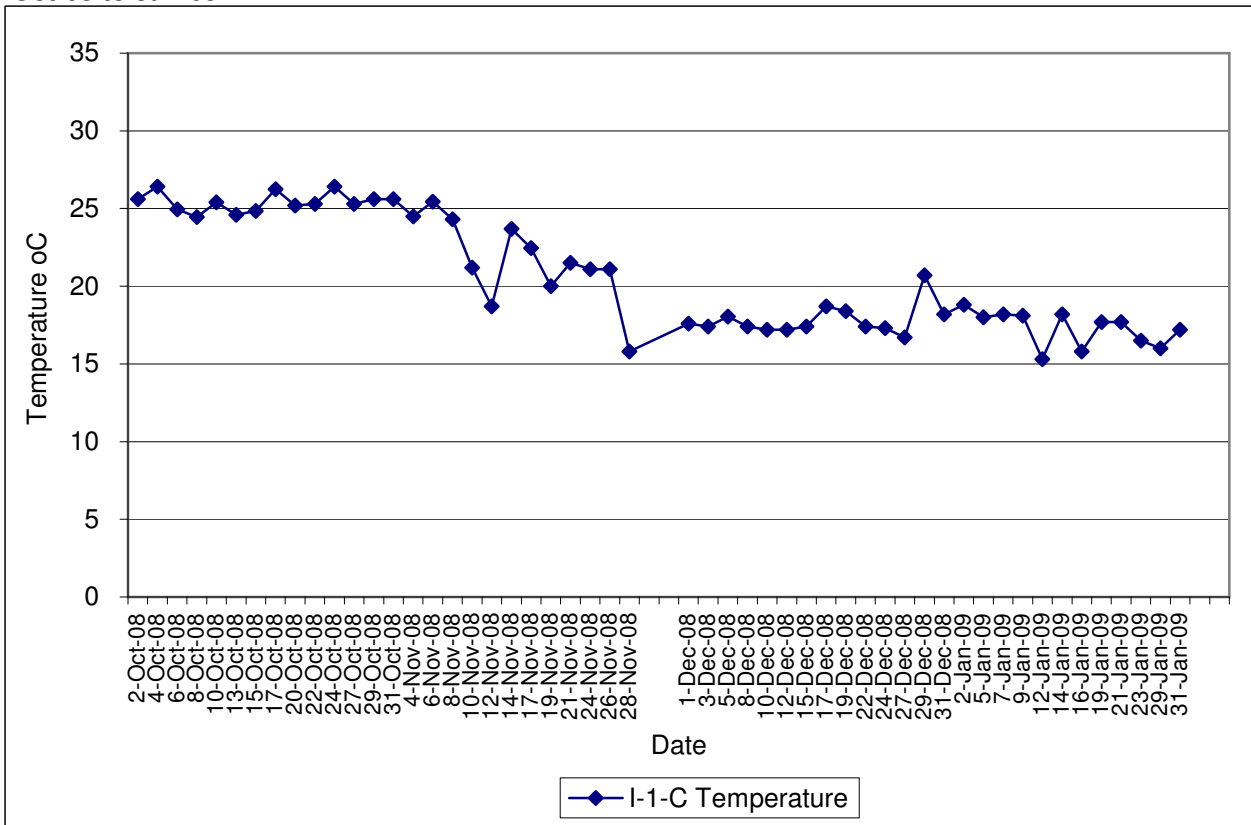


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Hong Hoi Chee Hong Temple (I-2)
Oct-08 to Jan-09

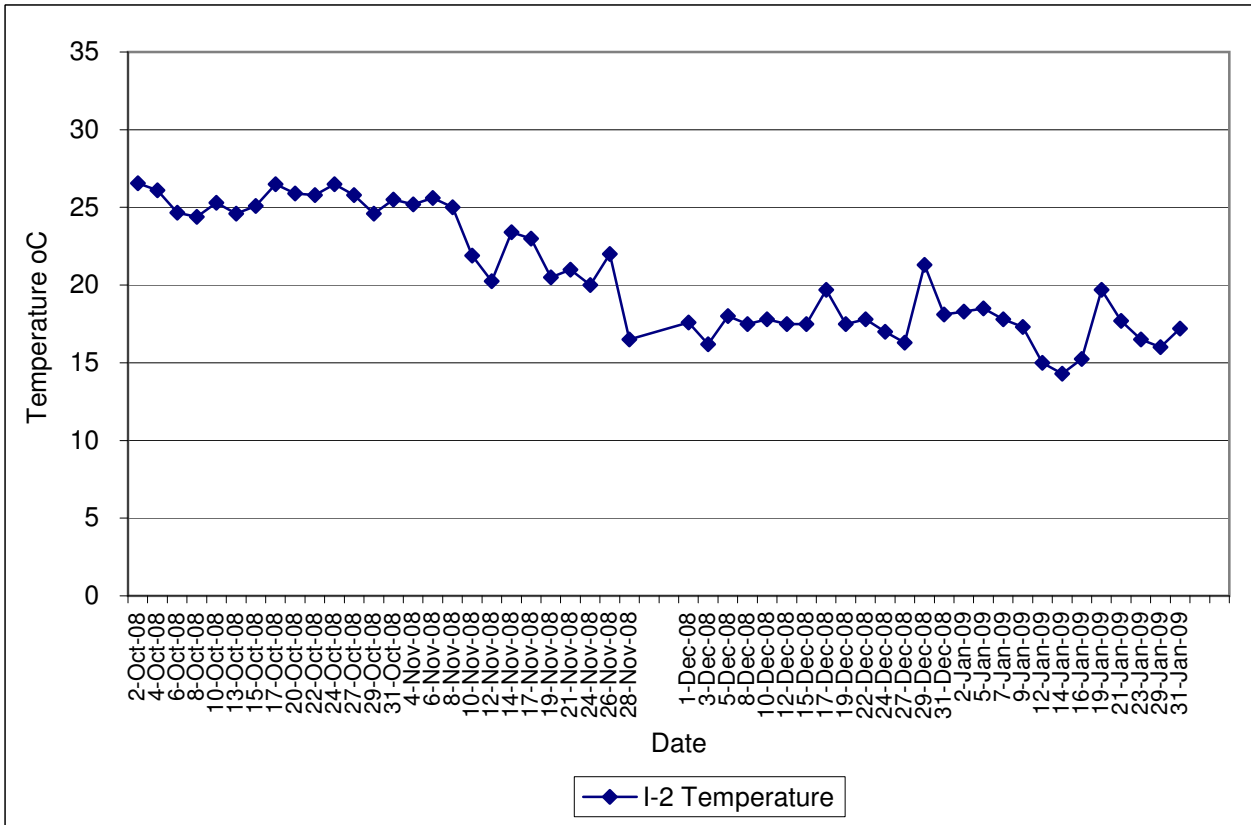


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Hong Hoi Chee Hong Temple (I-2-C)
Oct-08 to Jan-09

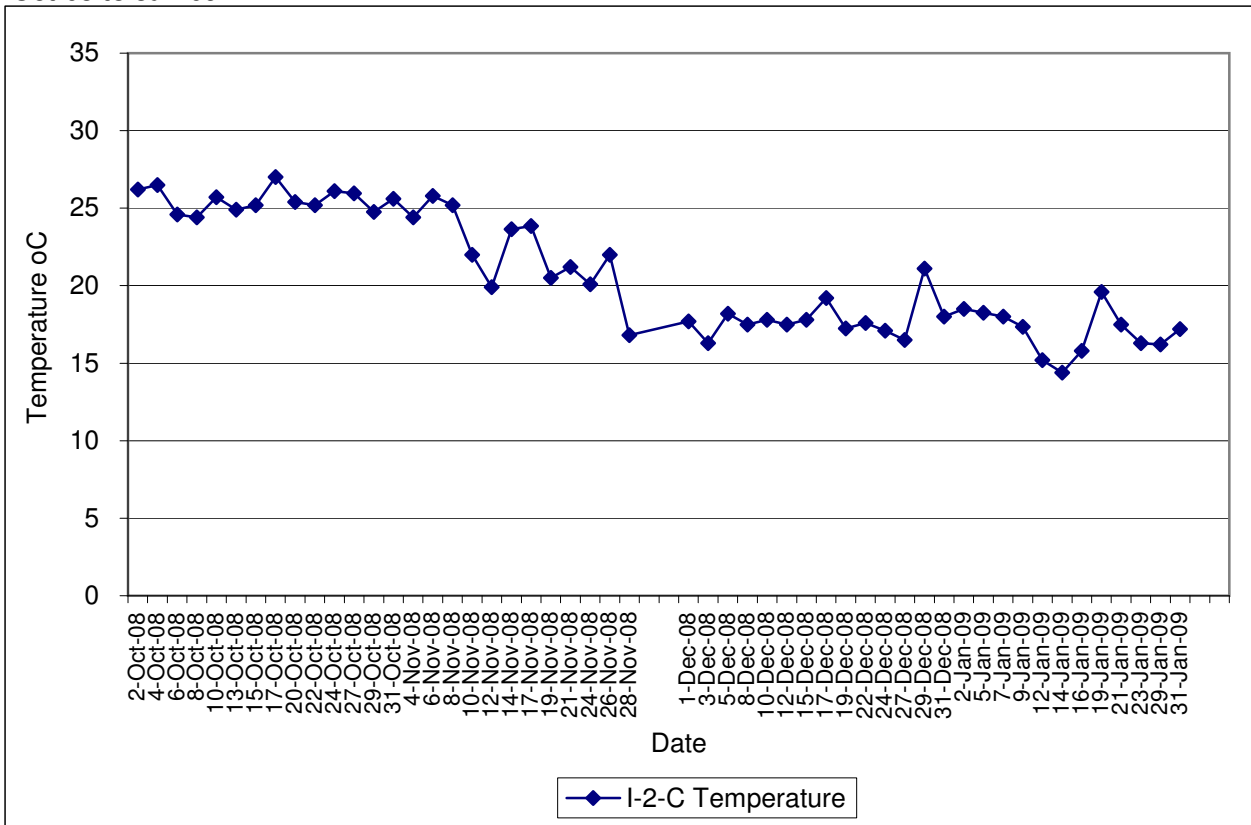


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Squatters (I-3)
Oct-08 to Jan-09

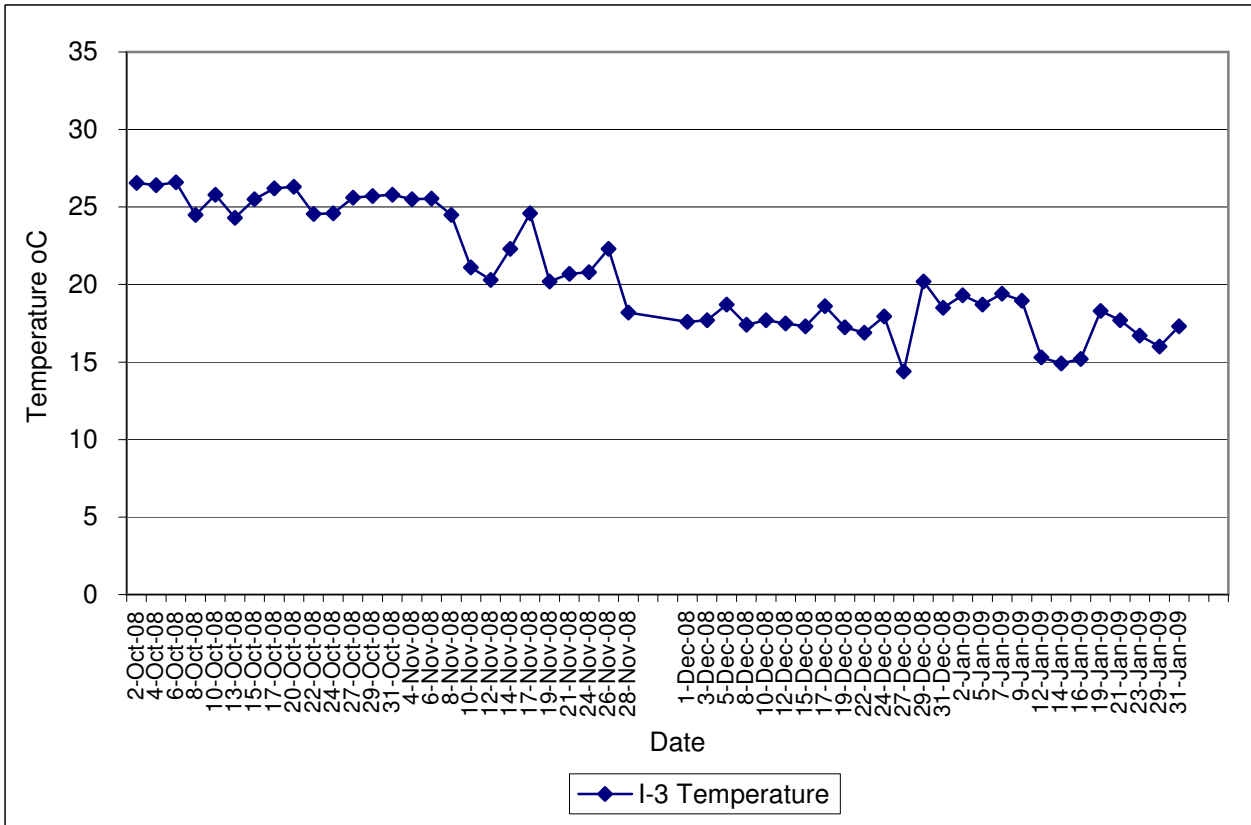


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Squatters (I-3-C)
Oct-08 to Jan-09

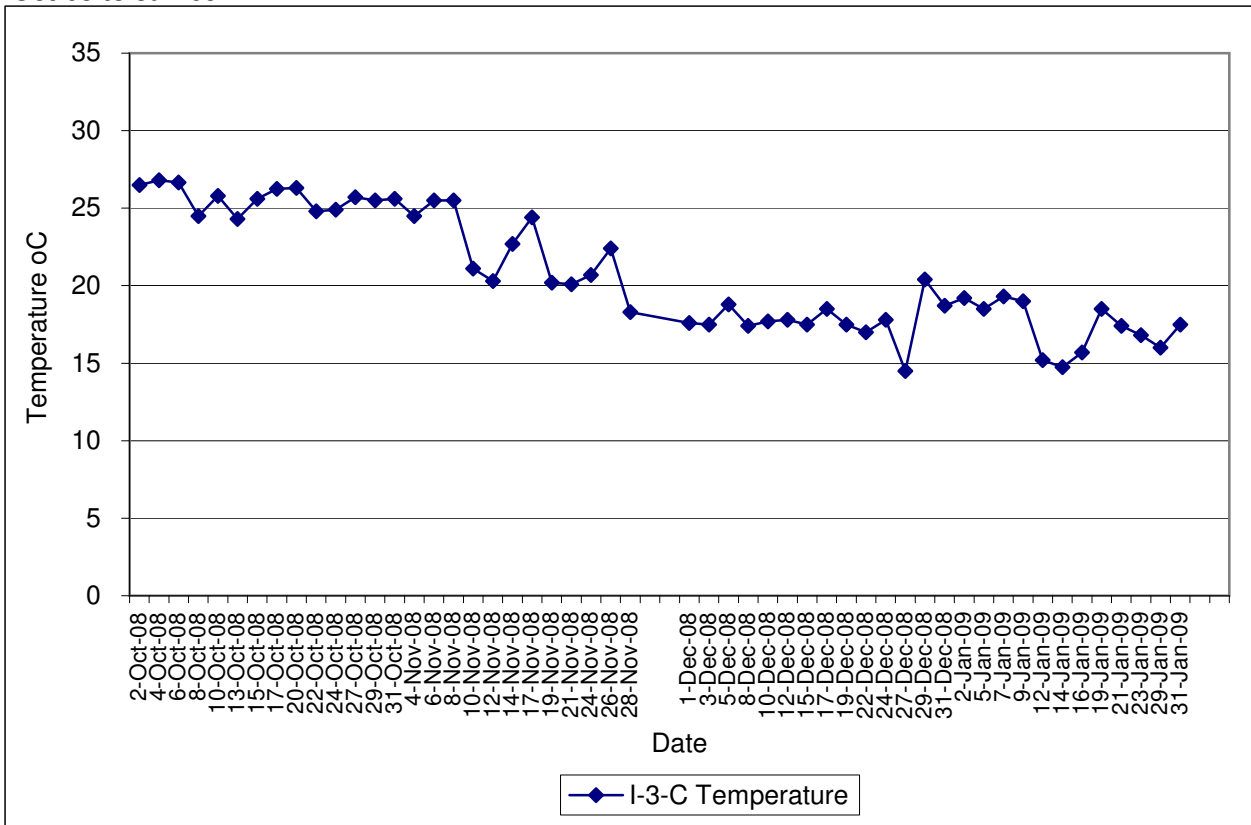


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Sik Sik Yuen Ho Fung College (I-1)
Oct-08 to Jan-09

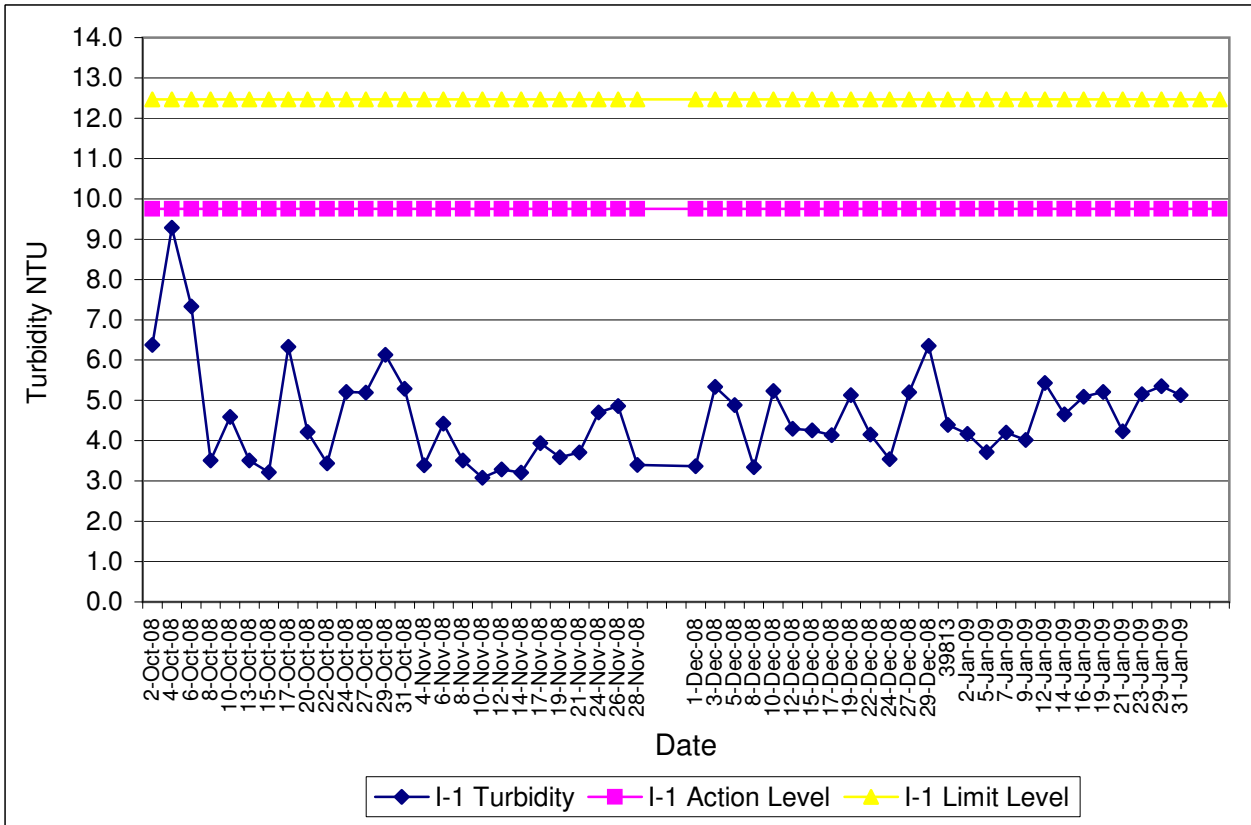


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Sik Sik Yuen Ho Fung College (I-1-C)
Oct-08 to Jan-09

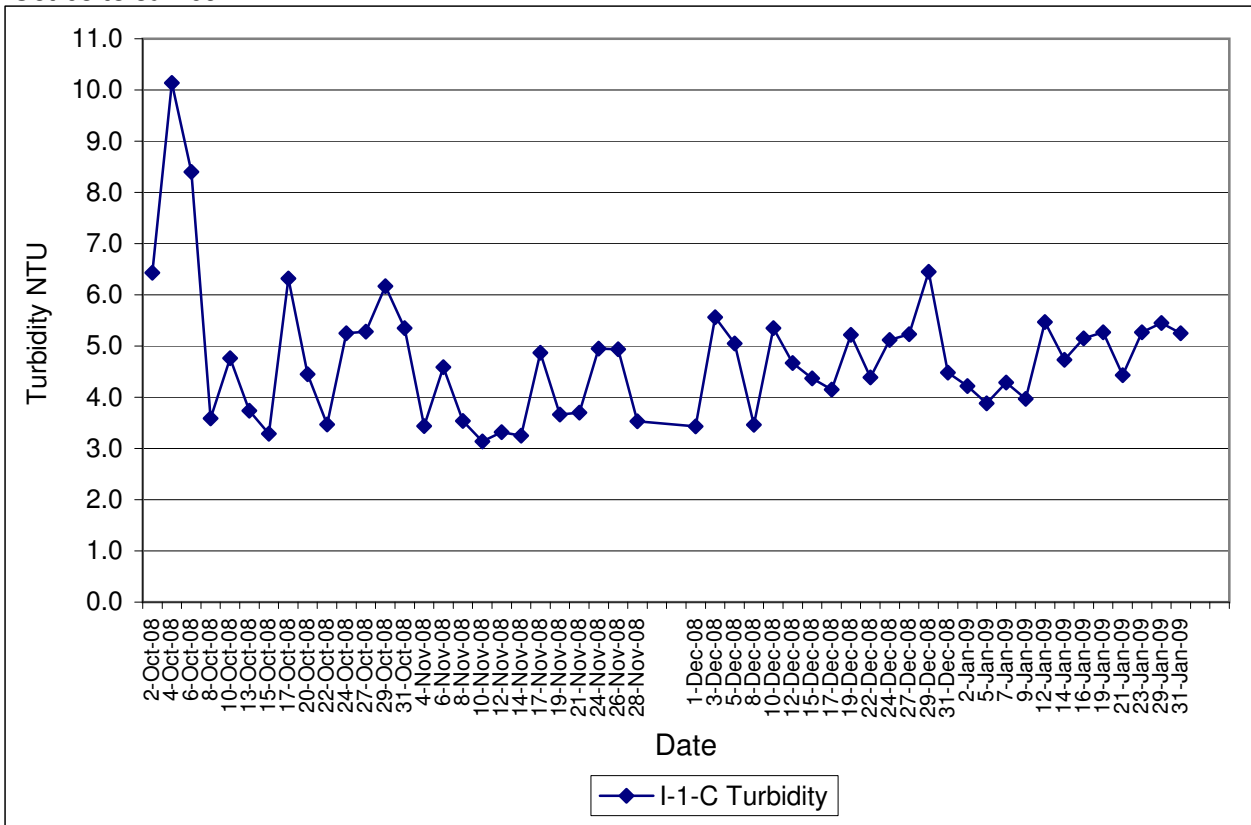


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Hong Hoi Chee Hong Temple (I-2)
Oct-08 to Jan-09

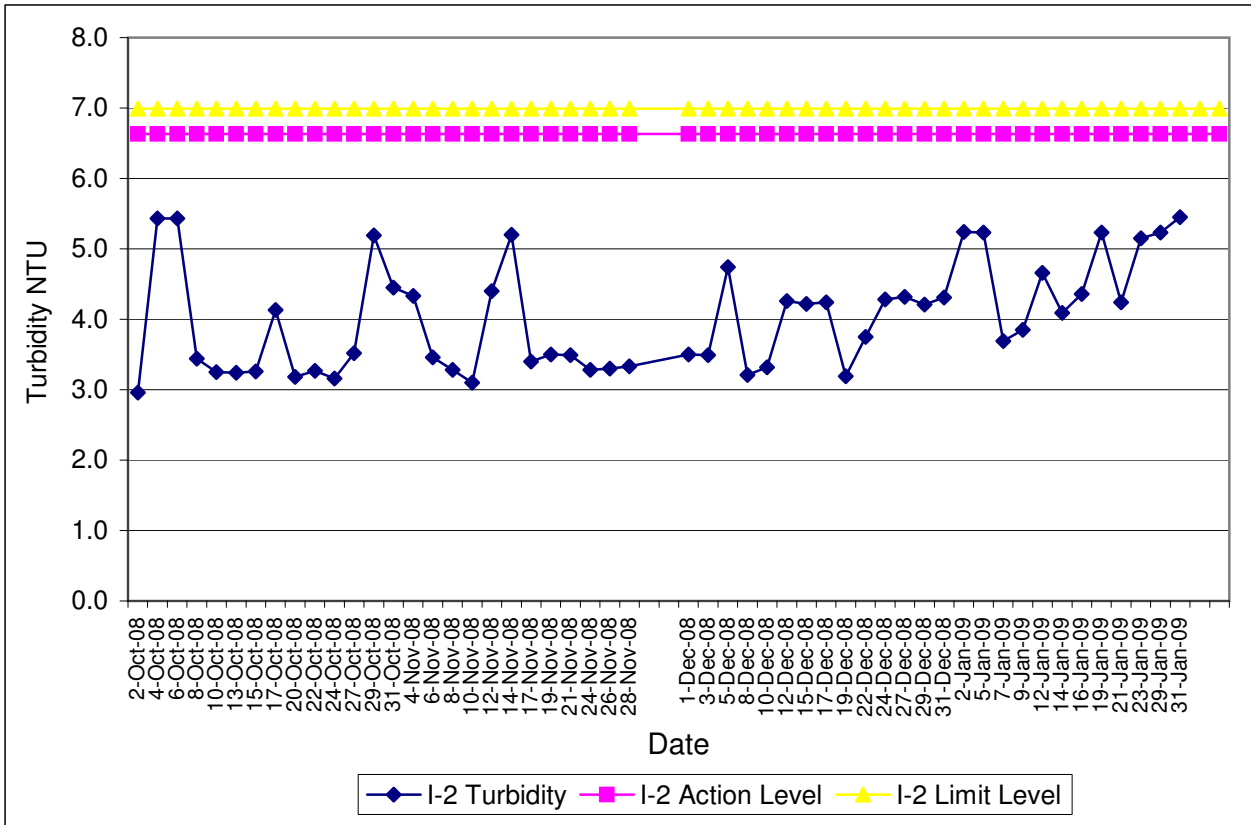


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Hong Hoi Chee Hong Temple (I-2-C)
Oct-08 to Jan-09

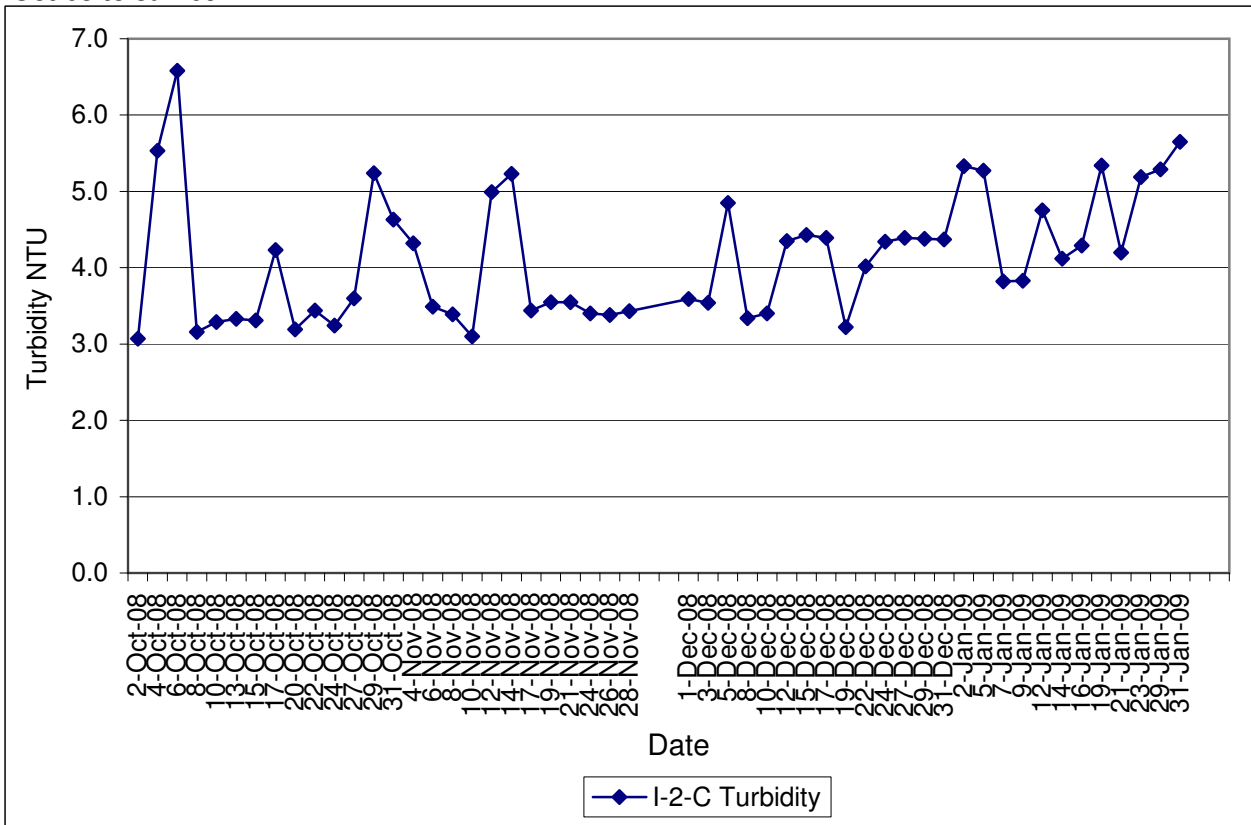

Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Squatters (I-3)
Oct-08 to Jan-09

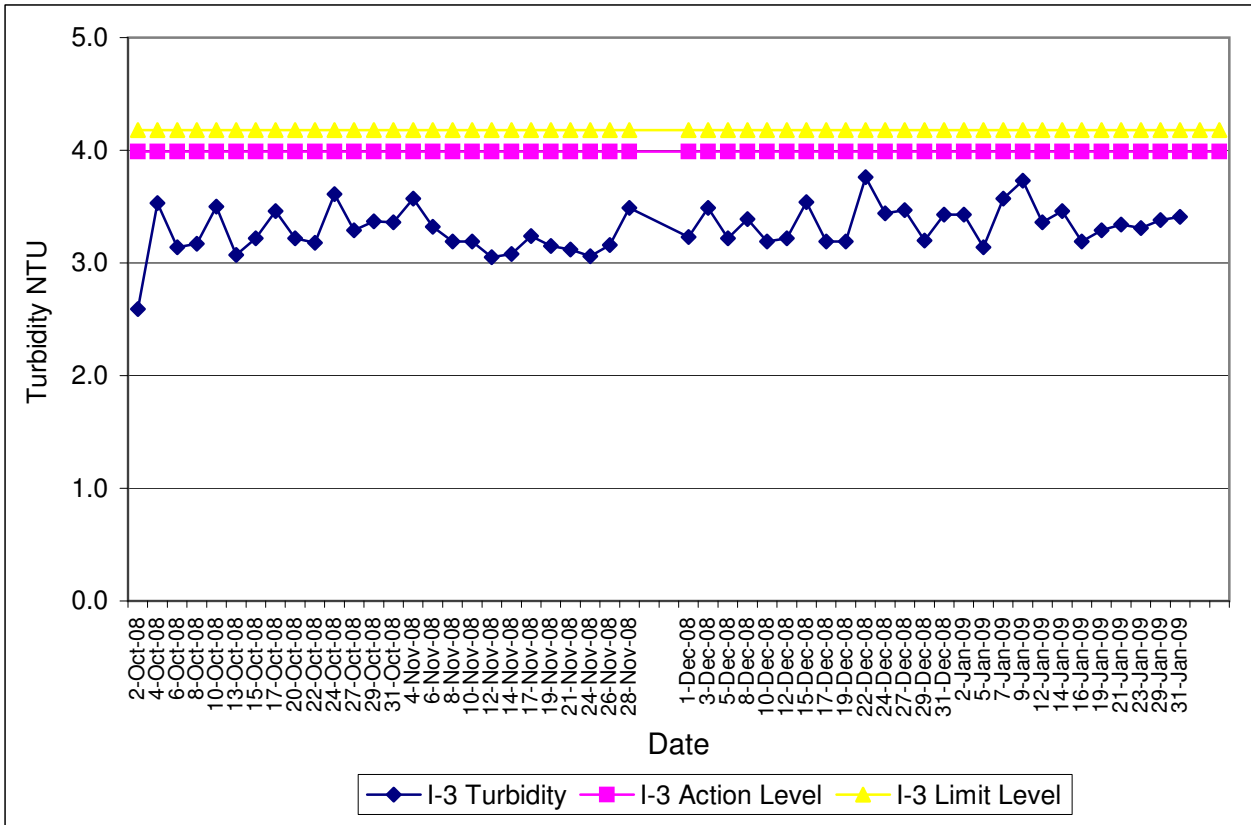


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Squatters (I-3-C)
Oct-08 to Jan-09

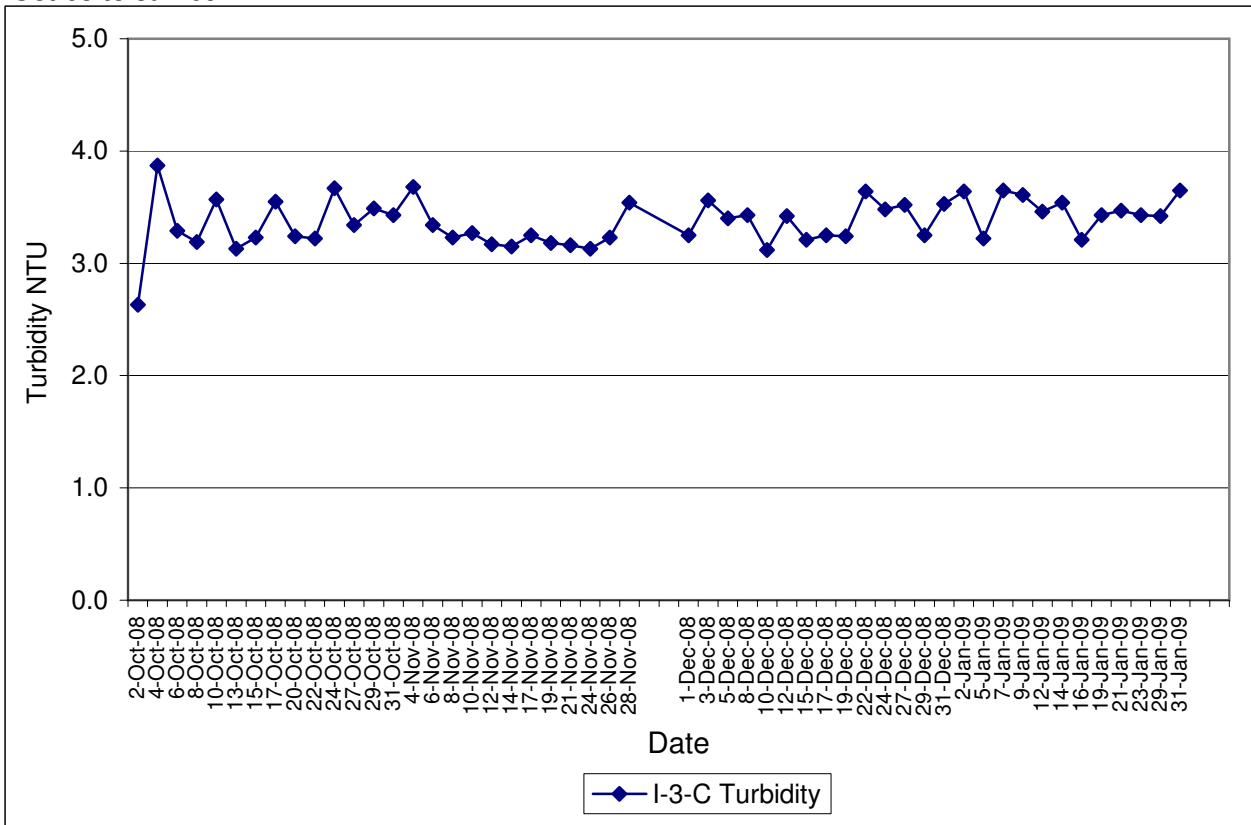


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Sik Sik Yuen Ho Fung College (I-1)
Oct-08 to Jan-09

Note: Exceedances of Action / Limit Levels occur when the levels of DO are below the respective limit levels.

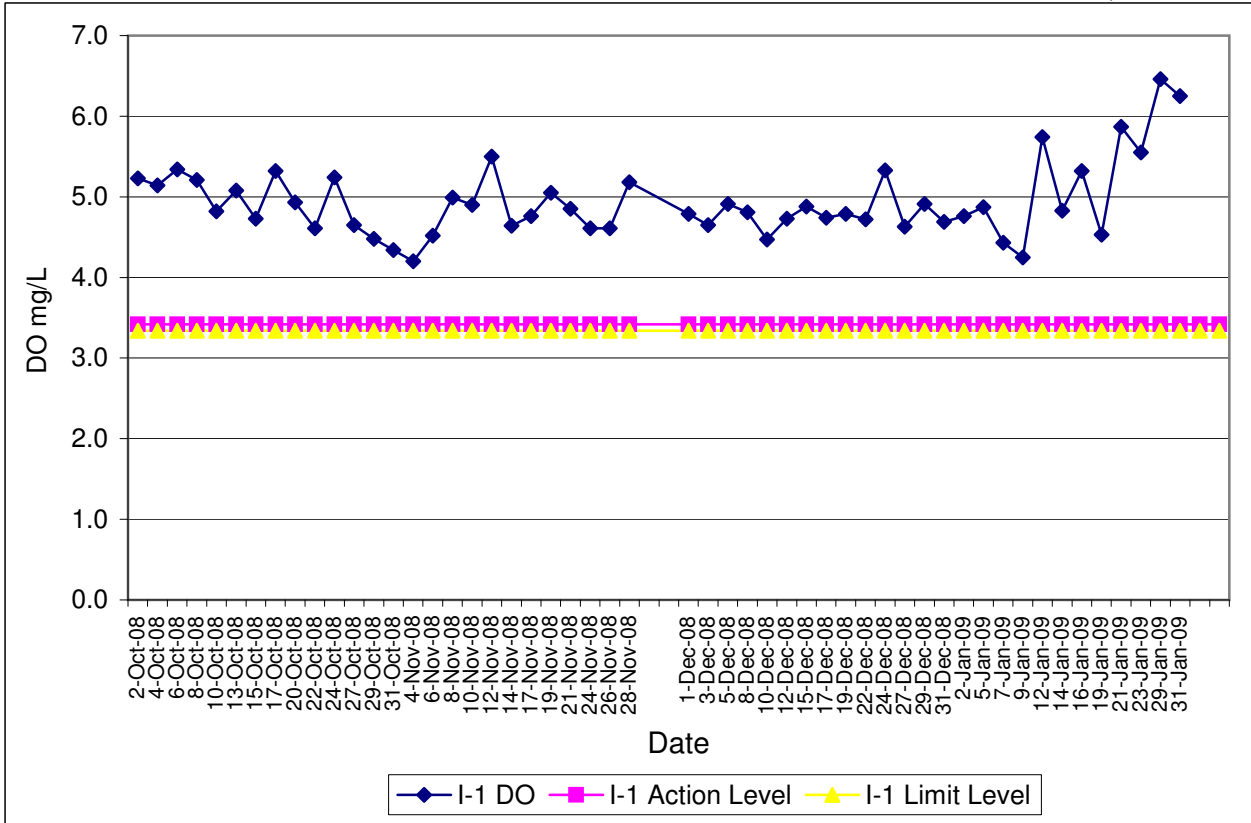


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Sik Sik Yuen Ho Fung College (I-1-C)
Oct-08 to Jan-09

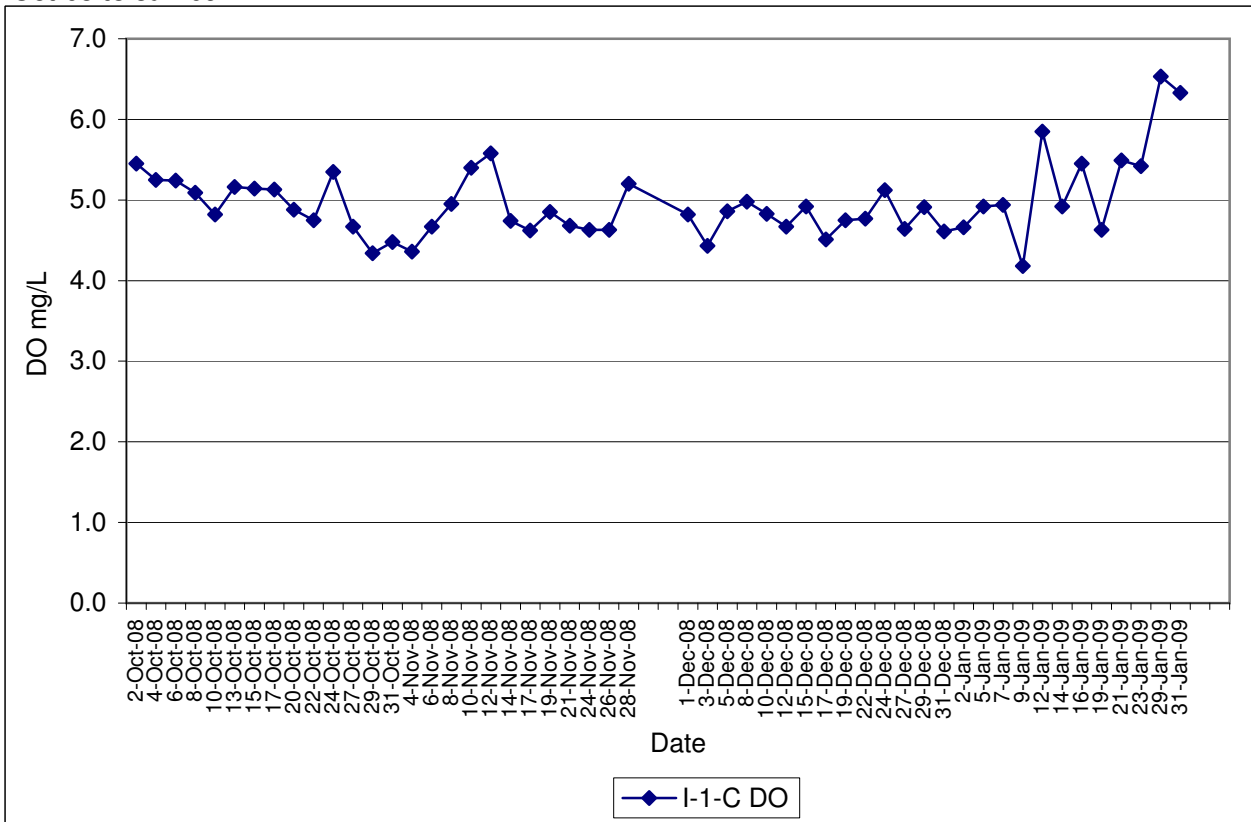

**Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Hong Hoi Chee Hong Temple (I-2)**


Oct-08 to Jan-09

Note: Exceedances of Action / Limit Levels occur when the levels of DO are below the respective limit levels.

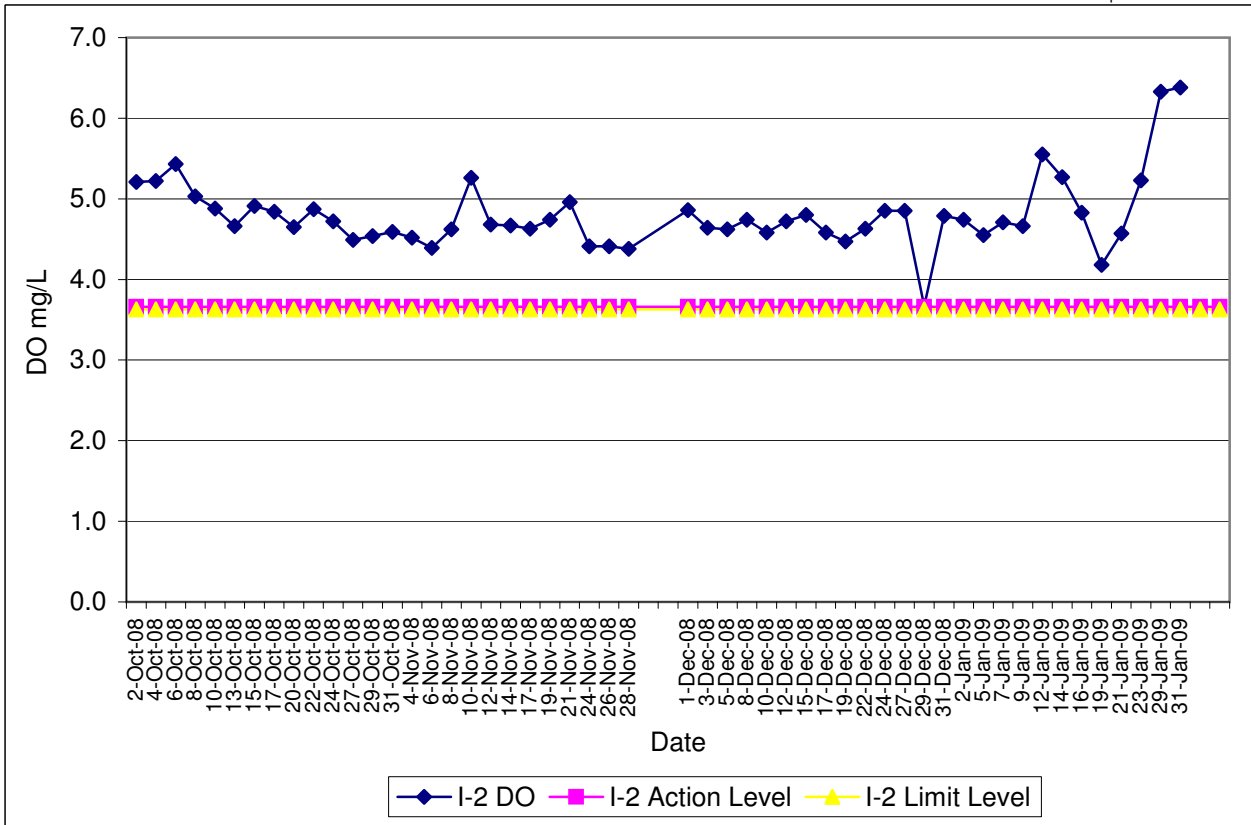

**Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Hong Hoi Chee Hong Temple (I-2-C)**


Oct-08 to Jan-09

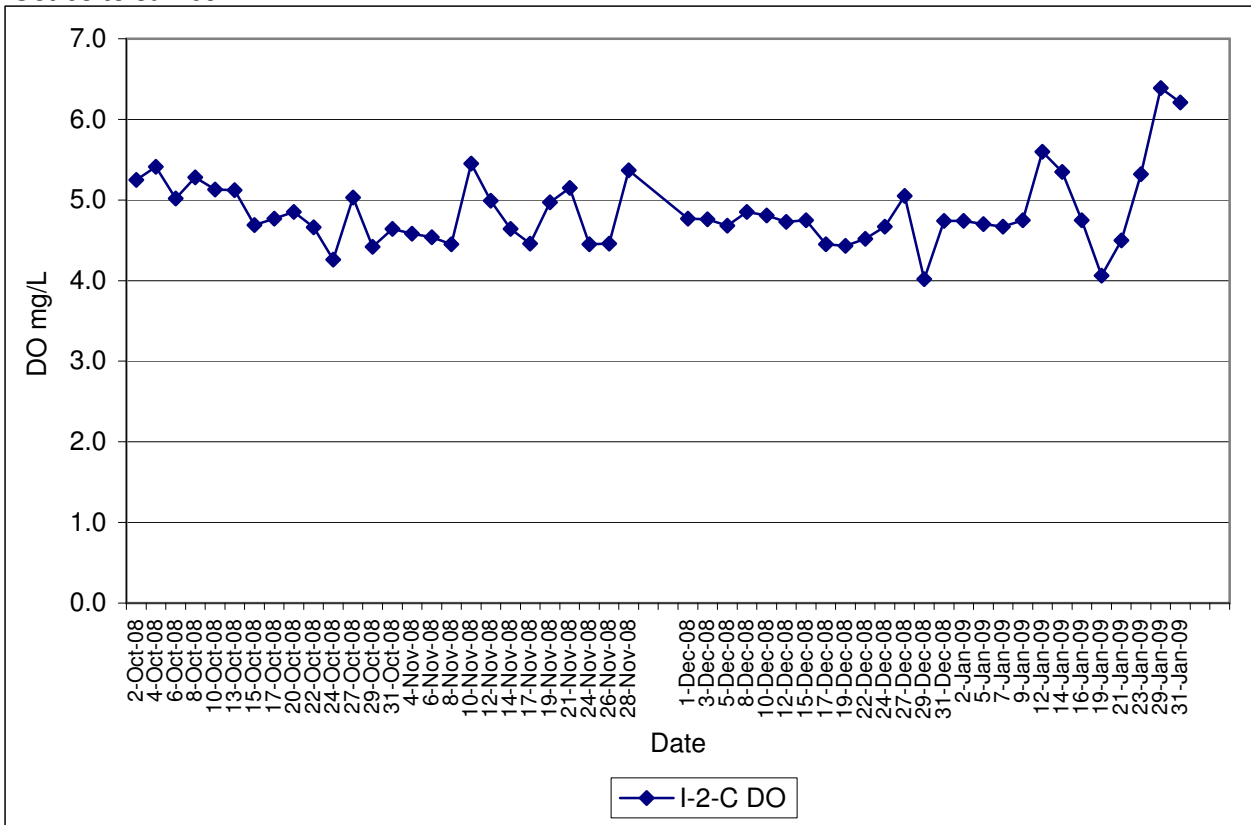

Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Squatters (I-3)


Oct-08 to Jan-09

Note: Exceedances of Action / Limit Levels occur when the levels of DO are below the respective limit levels.

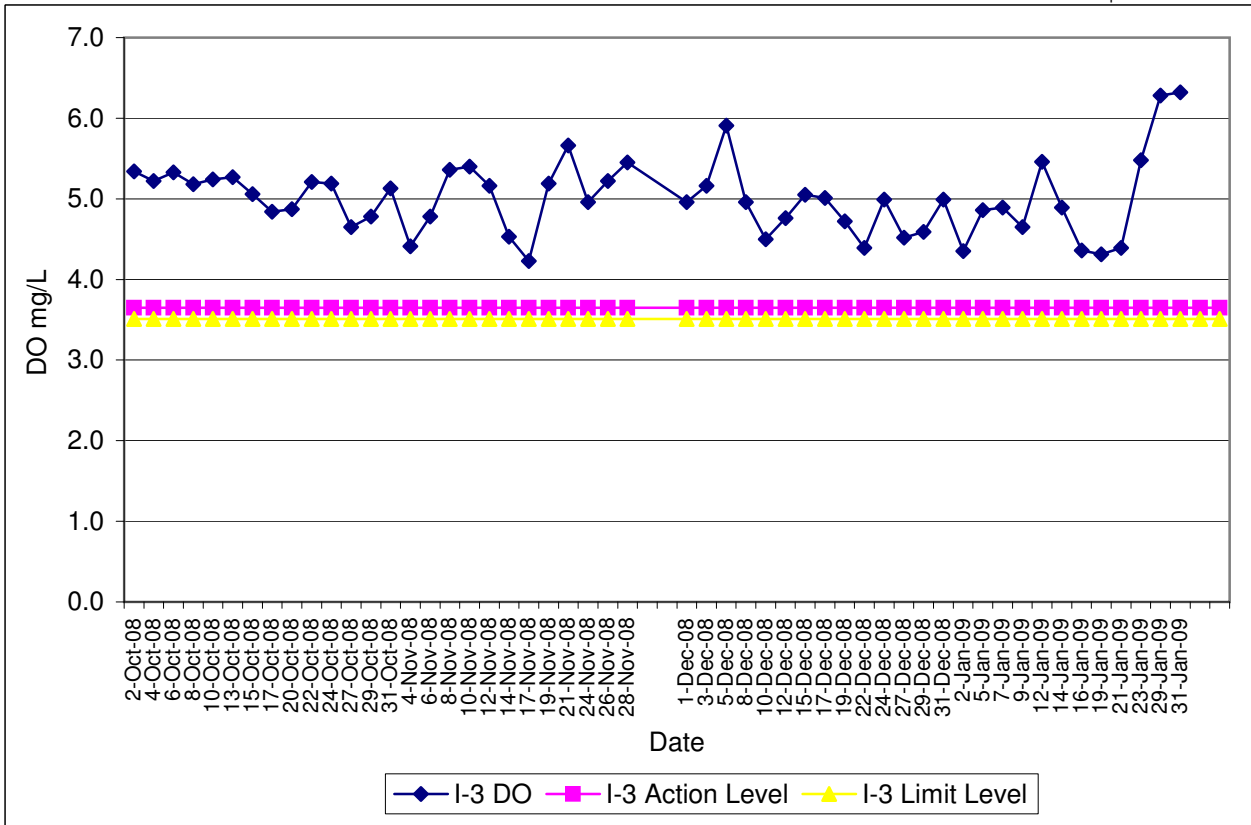


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Squatters (I-3-C)


Oct-08 to Jan-09

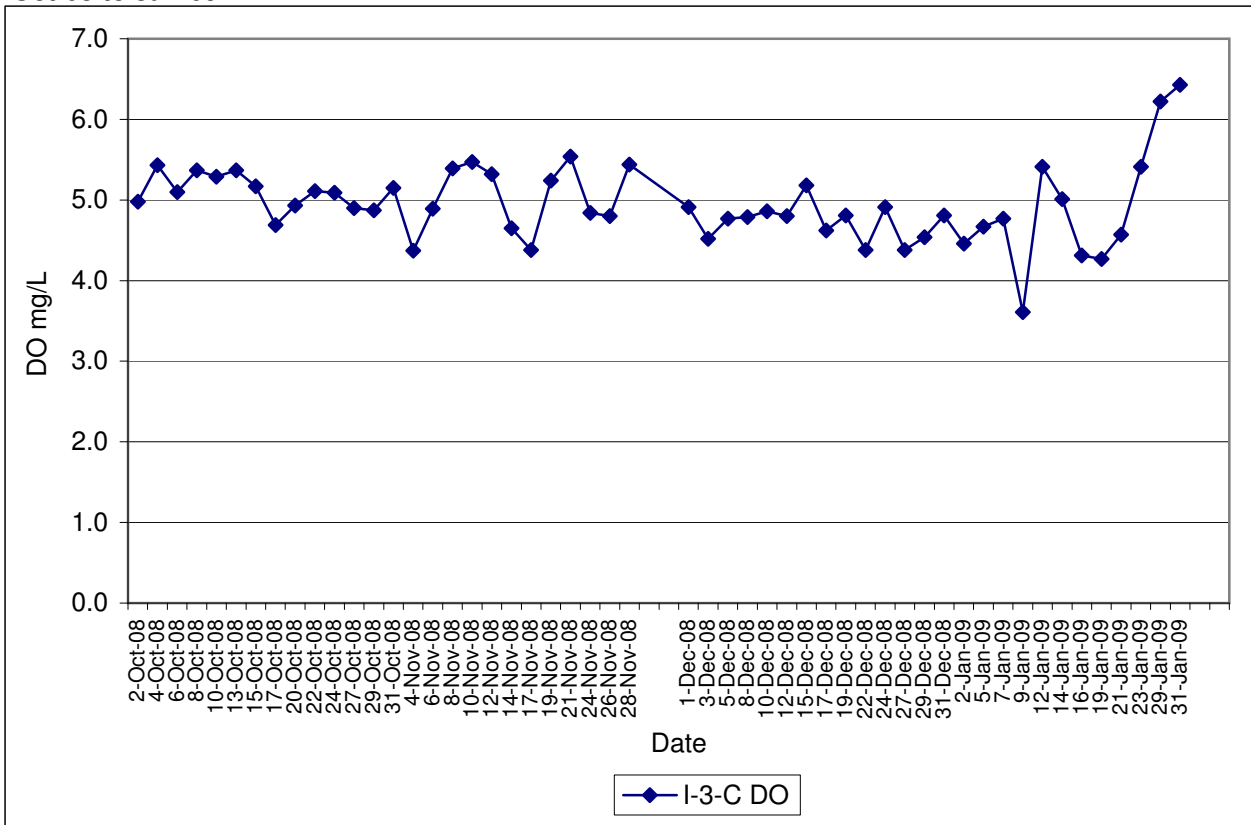


**Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
 Water Quality Results at Sik Sik Yuen Ho Fung College (I-1)
 Oct-08 to Jan-09**

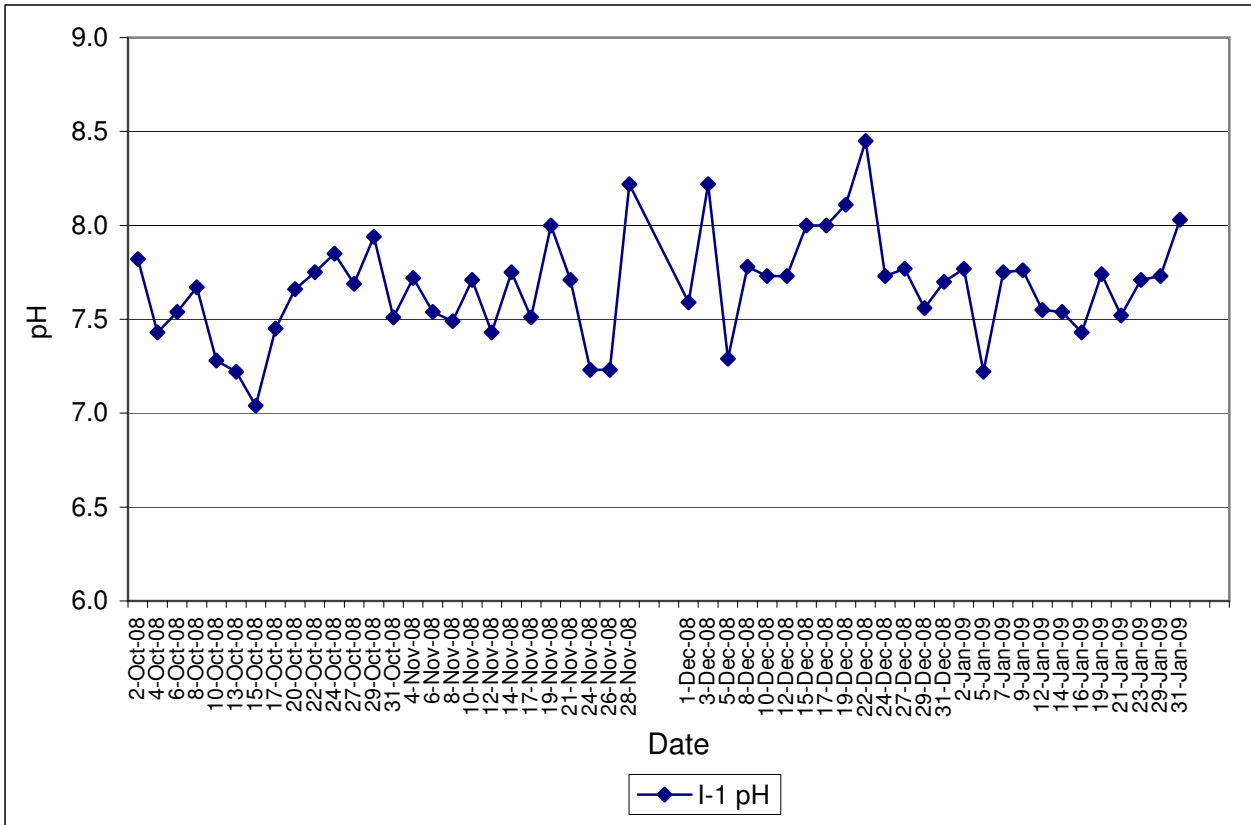


**Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
 Water Quality Results at Sik Sik Yuen Ho Fung College (I-1-C)
 Oct-08 to Jan-09**

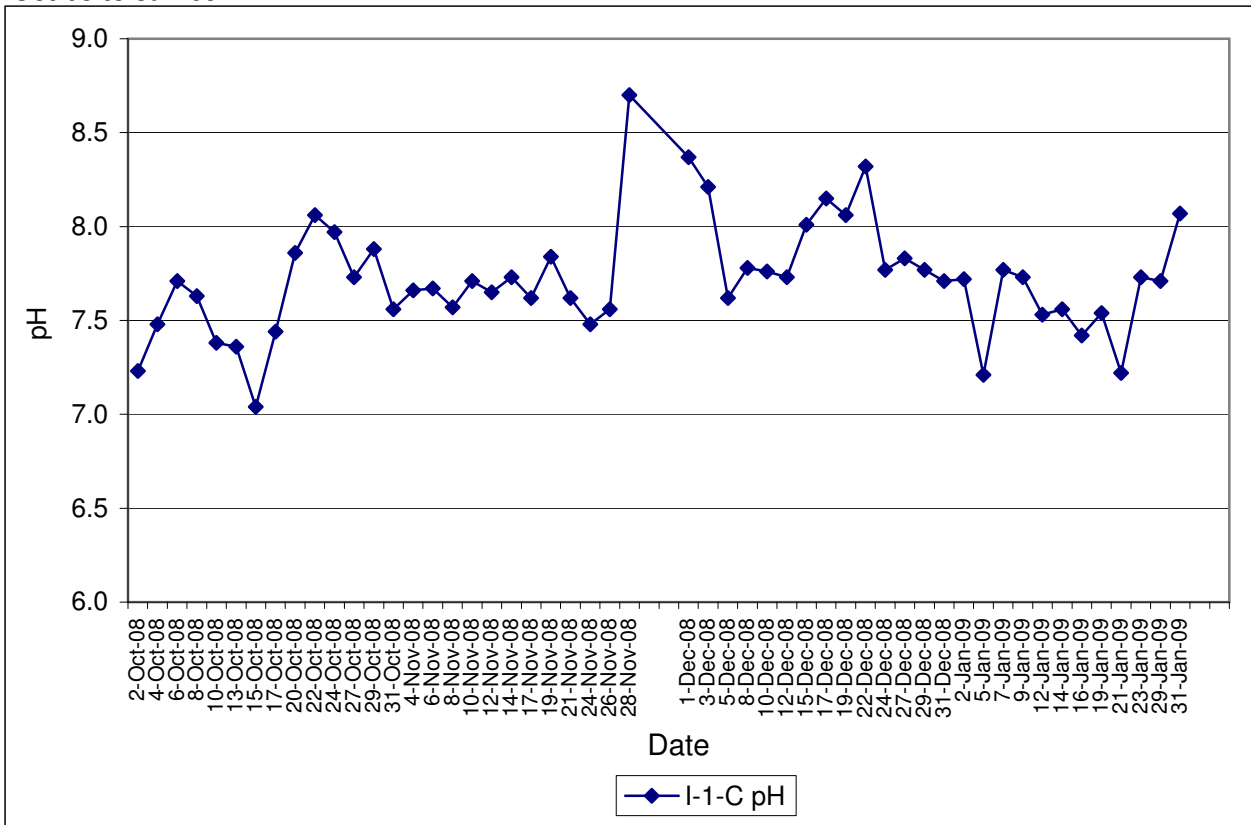


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Hong Hoi Chee Hong Temple (I-2)
Oct-08 to Jan-09

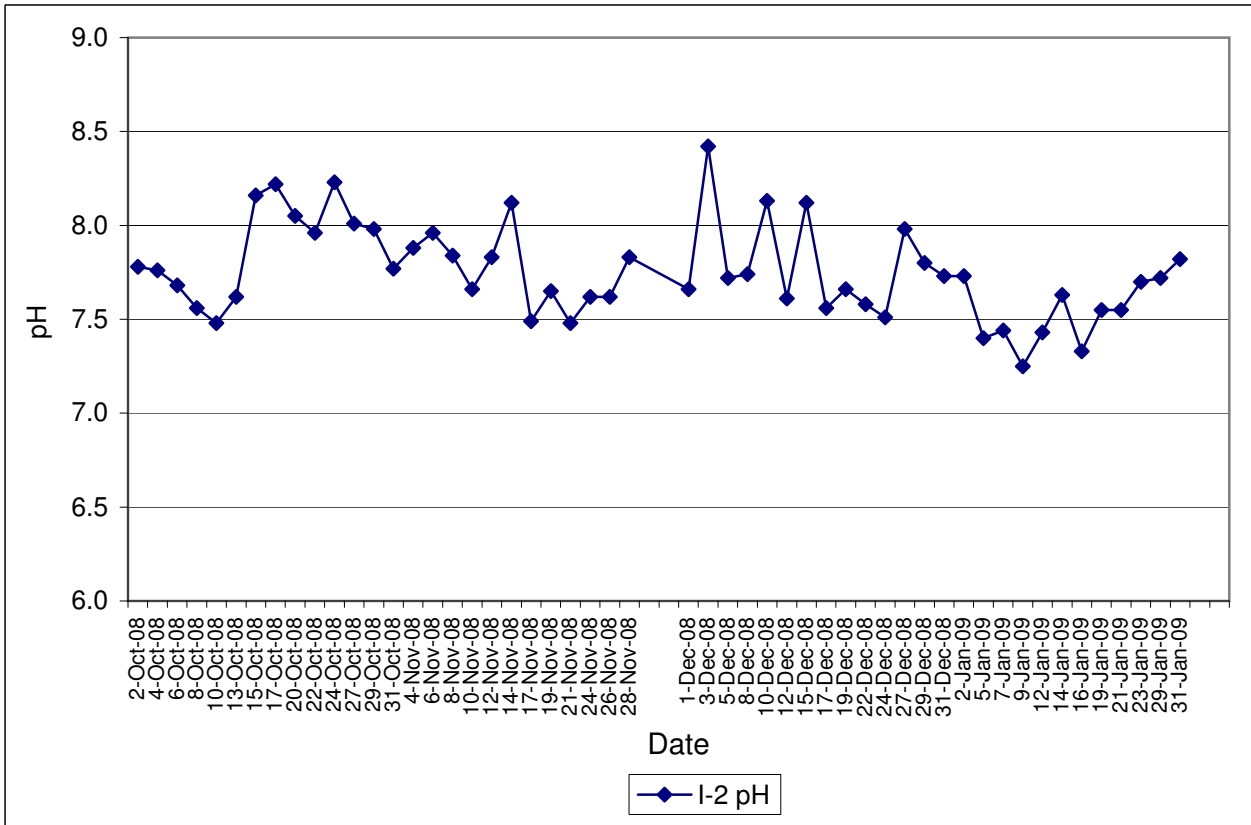


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Hong Hoi Chee Hong Temple (I-2-C)
Oct-08 to Jan-09

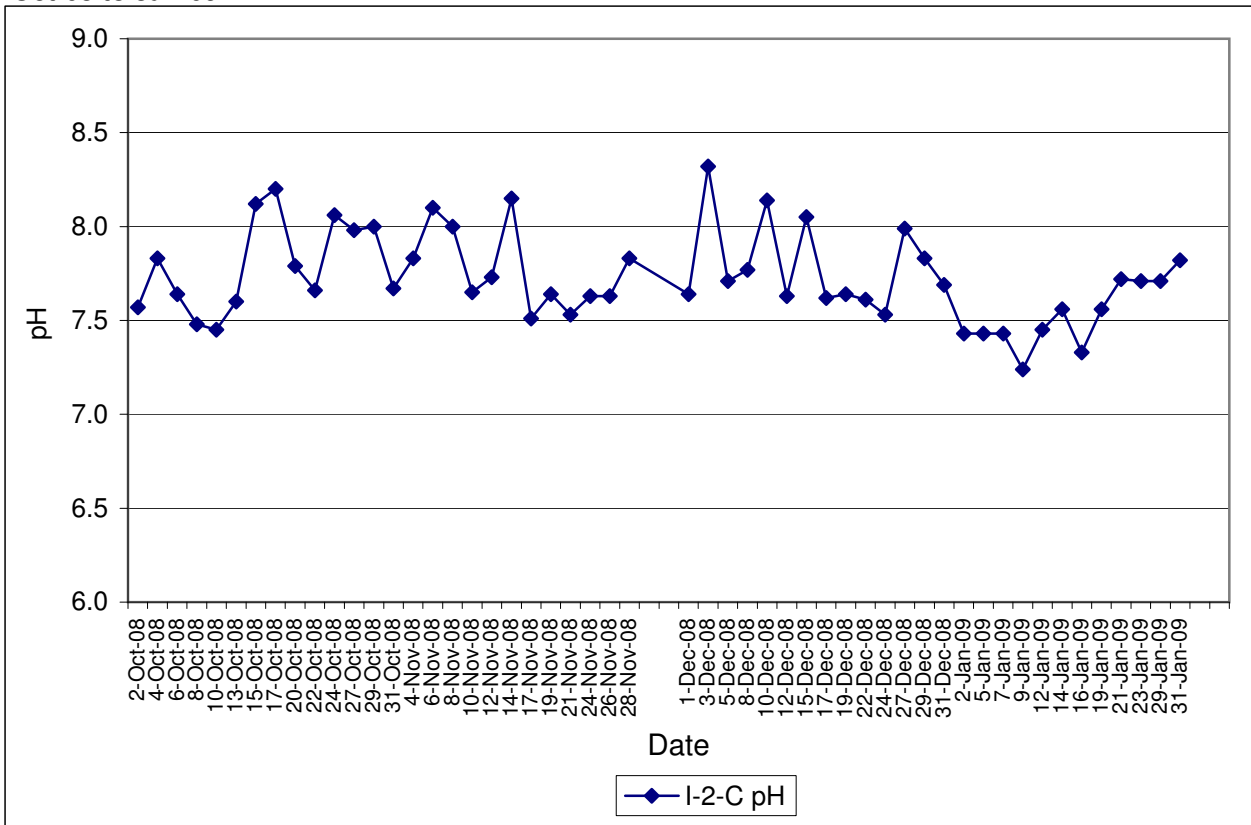


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Squatters (I-3)
Oct-08 to Jan-09

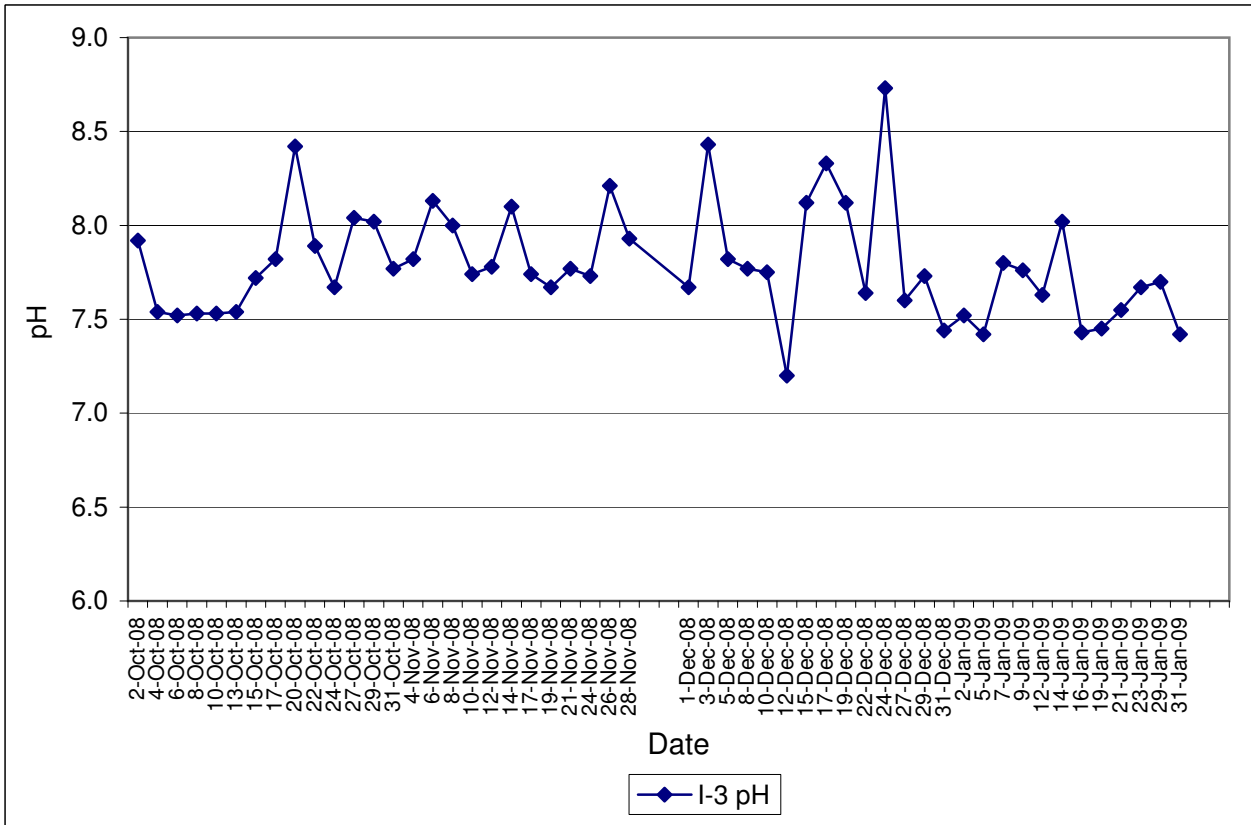


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Squatters (I-3-C)
Oct-08 to Jan-09

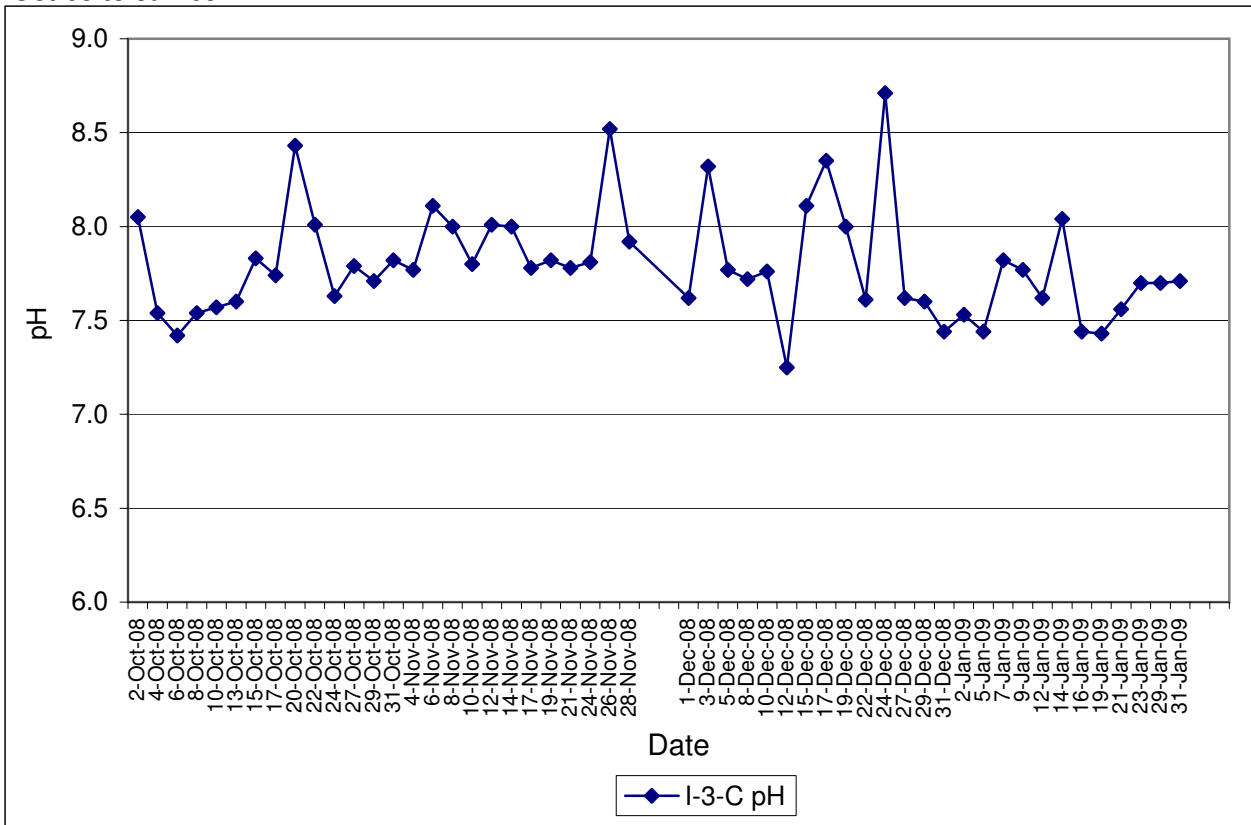


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Sik Sik Yuen Ho Fung College (I-1)
Oct-08 to Jan-09

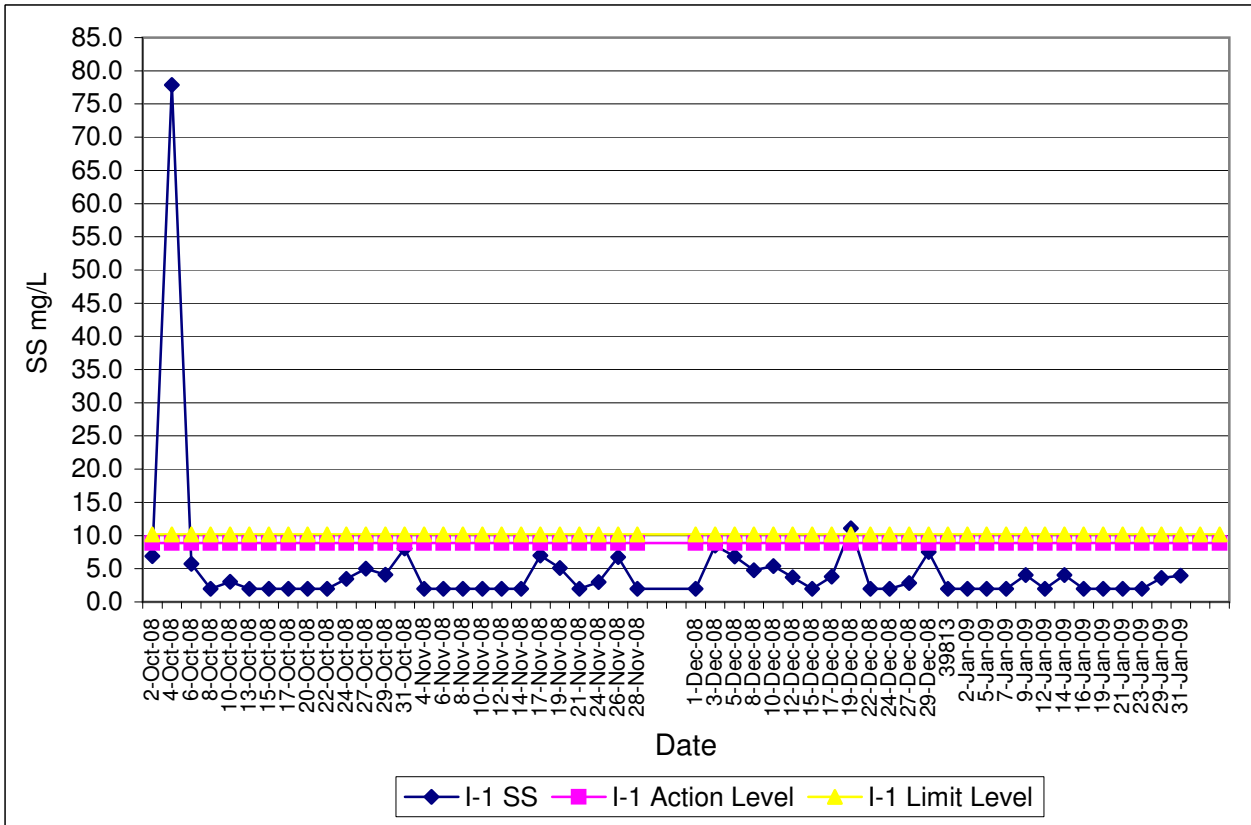


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Sik Sik Yuen Ho Fung College (I-1-C)
Oct-08 to Jan-09

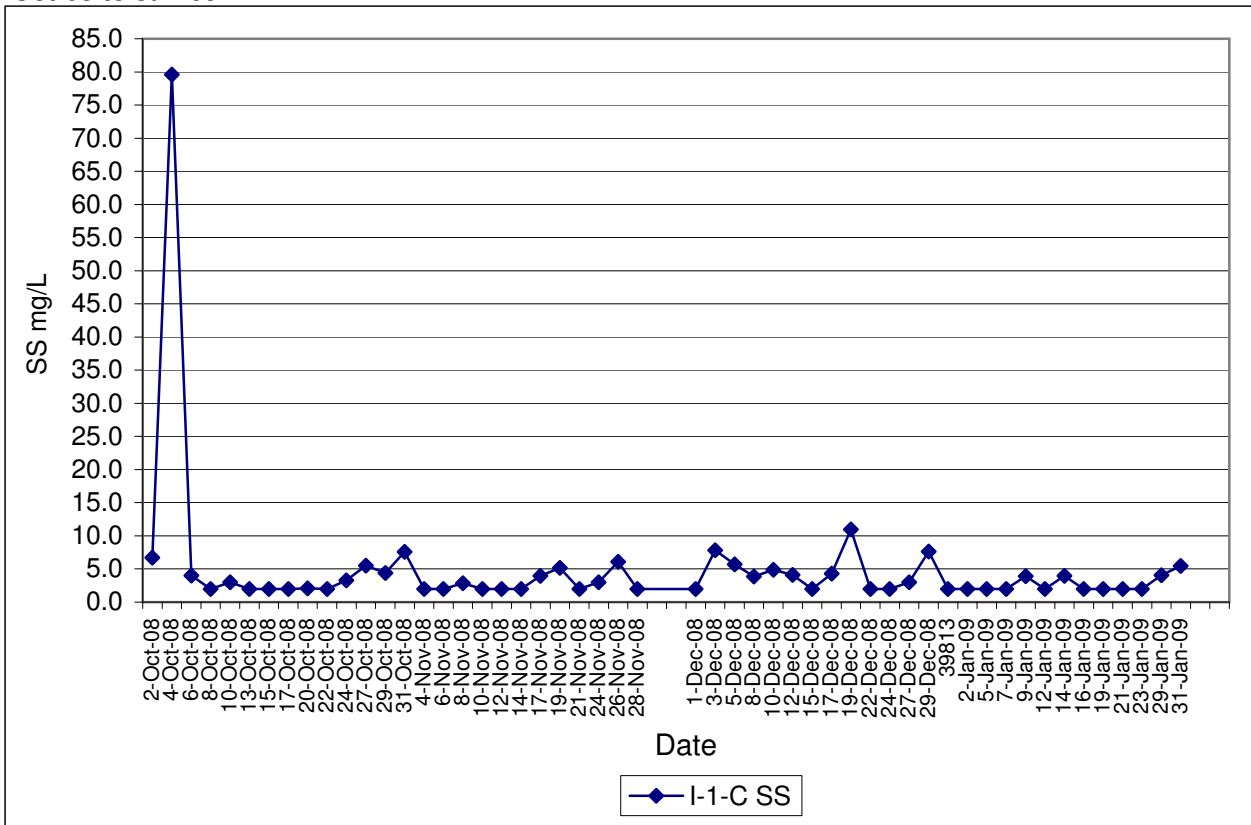


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Hong Hoi Chee Hong Temple (I-2)
Oct-08 to Jan-09

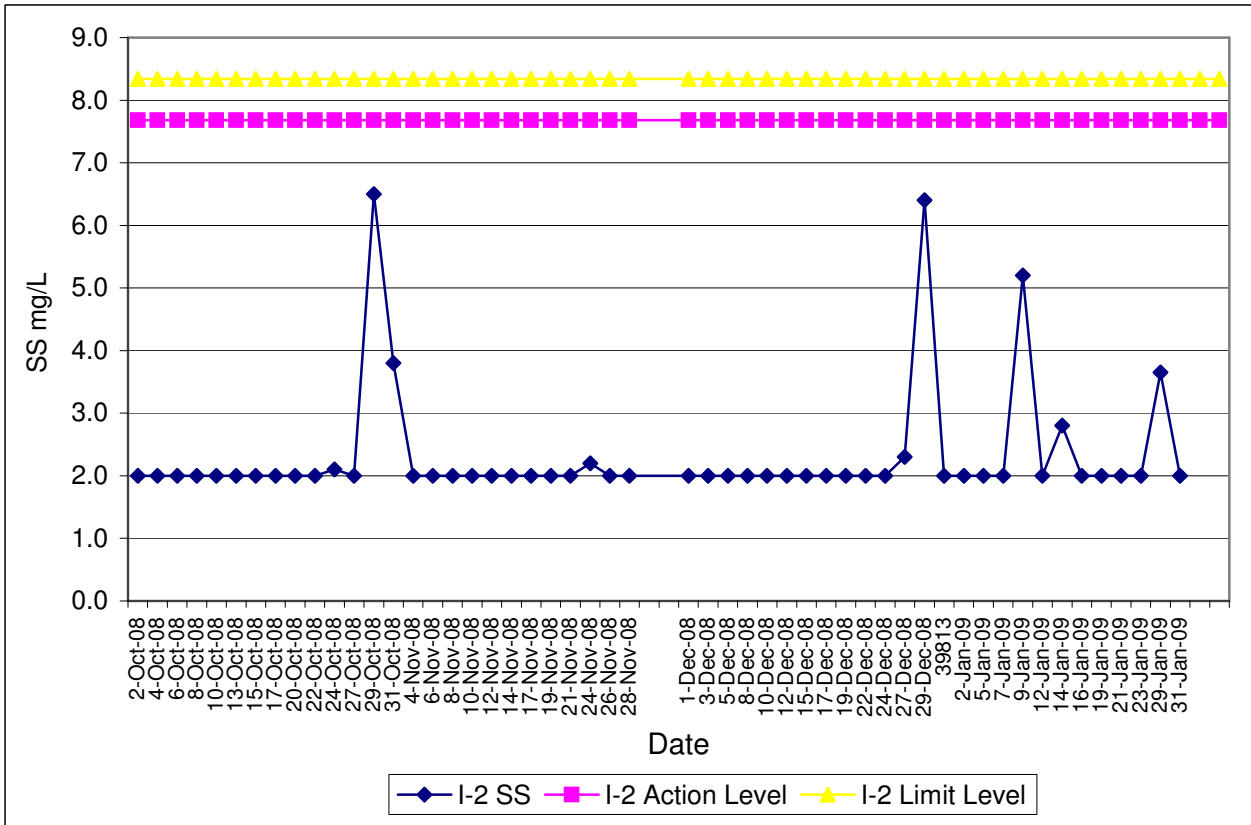

Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Hong Hoi Chee Hong Temple (I-2-C)
Oct-08 to Jan-09

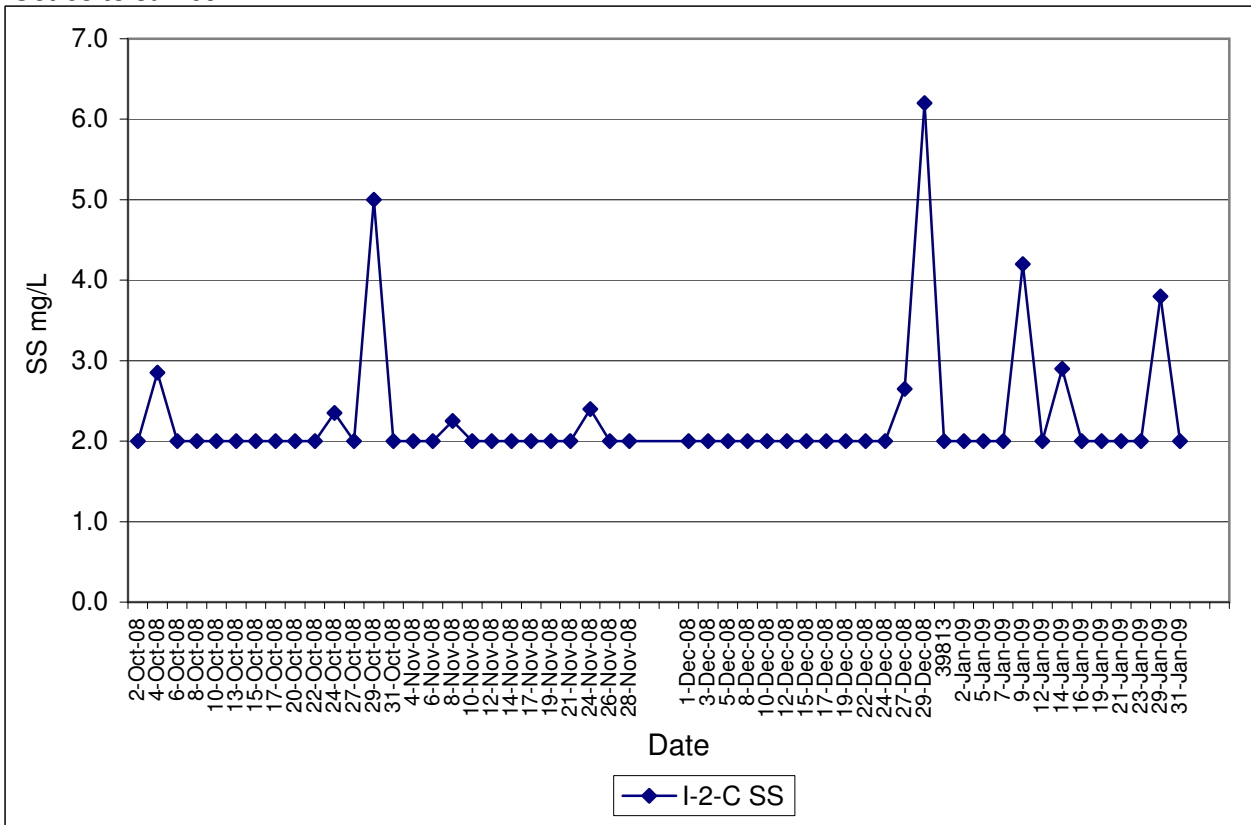

Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Squatters (I-3)
Oct-08 to Jan-09

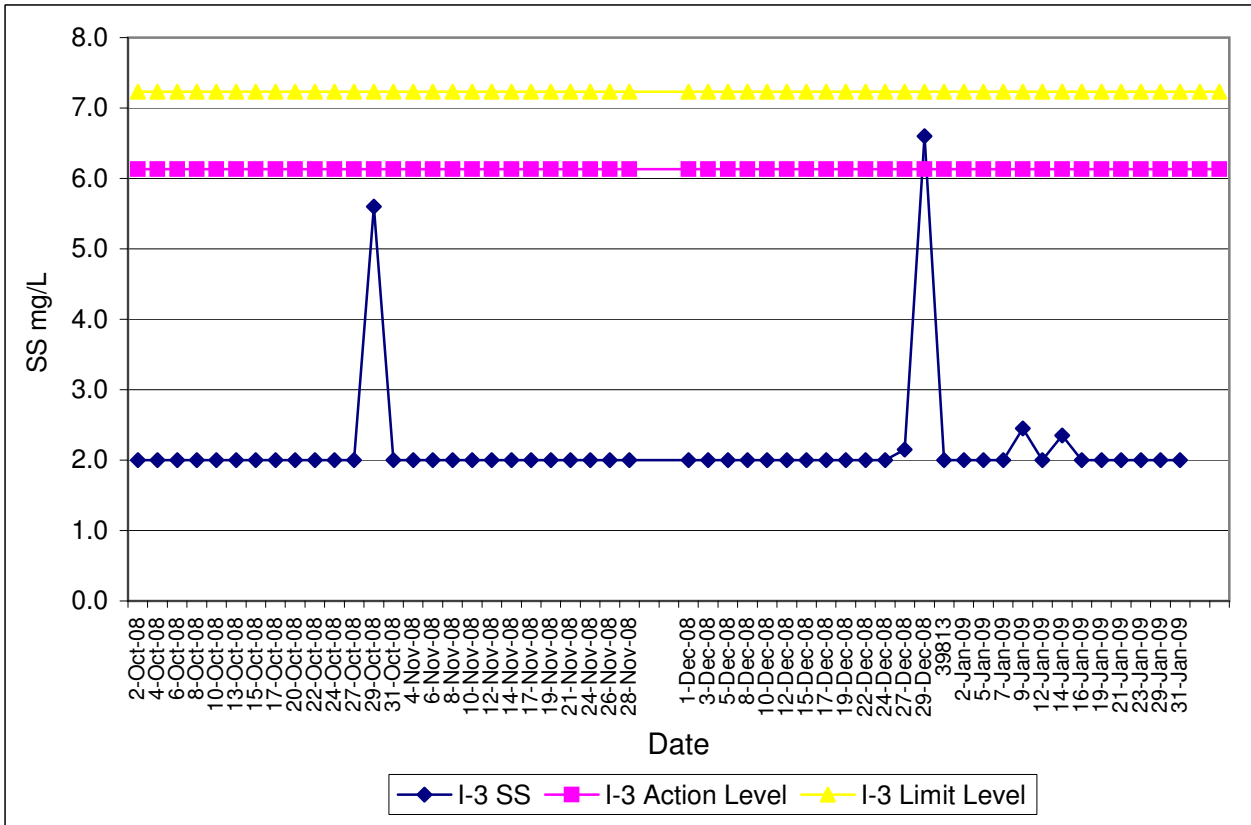

Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel
Water Quality Results at Squatters (I-3-C)
Oct-08 to Jan-09

